



**JOHN  
HOLLAND**

# INLAND RAIL

## ILLABO TO STOCKINBINGAL PROJECT

I2S | EPL Monthly Monitoring Report

Document Number: 6-0019-220-PES-00-RP-0001

Document Status: Issued for Use

Revision: 1



Document Control

|                   |                               |                                        |
|-------------------|-------------------------------|----------------------------------------|
| Document Title    | EPL Monthly Monitoring Report |                                        |
| IRPL Document No. | 6-0019-220-PES-00-RP-0001     |                                        |
| Prepared By       |                               |                                        |
| Document Owner    |                               |                                        |
|                   | REVIEWED BY                   | APPROVED BY                            |
| Name              |                               |                                        |
| Title             | Senior Environment Advisor    | Environment and Sustainability Manager |
| Signature<br>Date |                               |                                        |

Revision History

| REVISION | DATE ISSUED | DESCRIPTION    |
|----------|-------------|----------------|
| 0        | 18/06/2026  | Issued for Use |
| 1        | 08/07/2026  | Issued for Use |
|          |             |                |
|          |             |                |



Table of Contents

**1 Introduction ..... 4**

1.1 The Project ..... 4

1.2 Report Scope..... 7

1.3 Reporting Requirements ..... 7

**2 Monitoring..... 11**

2.1 Weather ..... 11

2.2 Water ..... 13

2.3 Noise ..... 14

2.4 Blasting..... 17

2.5 Pollution Complaints..... 18

**Appendix A Premise Maps ..... 20**

**Appendix B EPL Water Discharge Points ..... 21**



# 1 Introduction

## 1.1 The Project

The Project is located in south-western New South Wales (NSW) in the Riverina region (refer to Figure 1-1). Illabo is a small town located at the southern end of the alignment 16 kilometres (km) north-east of Junee in the Junee Local Government Area (LGA).

Stockinbingal is situated at the northern end of the Project, approximately 20 km north-west of Cootamundra in the Cootamundra–Gundagai Regional LGA. The major towns surrounding the Project are Wagga Wagga, about 50 km to the south, Young to the north-east and Cootamundra to the east.

The Project comprises a new rail corridor that would connect Illabo to Stockinbingal. The alignment branches out from the existing rail line north-east of Illabo and travels north to join the Stockinbingal–Parkes Line west of Stockinbingal. The route will travel primarily through undeveloped land predominantly used for agriculture.

The Project includes modifications to the tie-in points at Illabo and Stockinbingal to allow for trains to safely enter and exit the Illabo to Stockinbingal section of Inland Rail. The alignment also crosses several local and private roads, watercourses and privately owned properties. Additionally, no major towns are located within the Project site between Illabo and Stockinbingal.

The Project will include a total extent of approximately 42.5 km, including 39 km of new, greenfield railway which will incorporate the following key features:

- single track standard gauge on a combination of existing ground level embankments and within cuttings
- new bridges and road overpasses
- crossing loop and maintenance siding
- new level crossings, stock crossings and upgrades to existing level crossings
- new major stormwater diversion and minor drainage works associated with installation and upgrades to culverts.

The Project will also include upgrades to approximately 3 km of existing track associated with tie-in works and construction of an additional 1.7 km of new track to maintain the existing rail network connections. Road upgrade works will also be undertaken to re-align approximately 1.4 km of Burley Griffin Way to provide a road-over-rail bridge at Stockinbingal. Re-alignment of Ironbong Road will also be completed to allow for safe sight lines. A temporary workforce accommodation camp will also be constructed to house the workforce for the duration of the Project.

Project locality and key features of the Project are shown on Figure 3-1 and **Error! Reference source not found..**

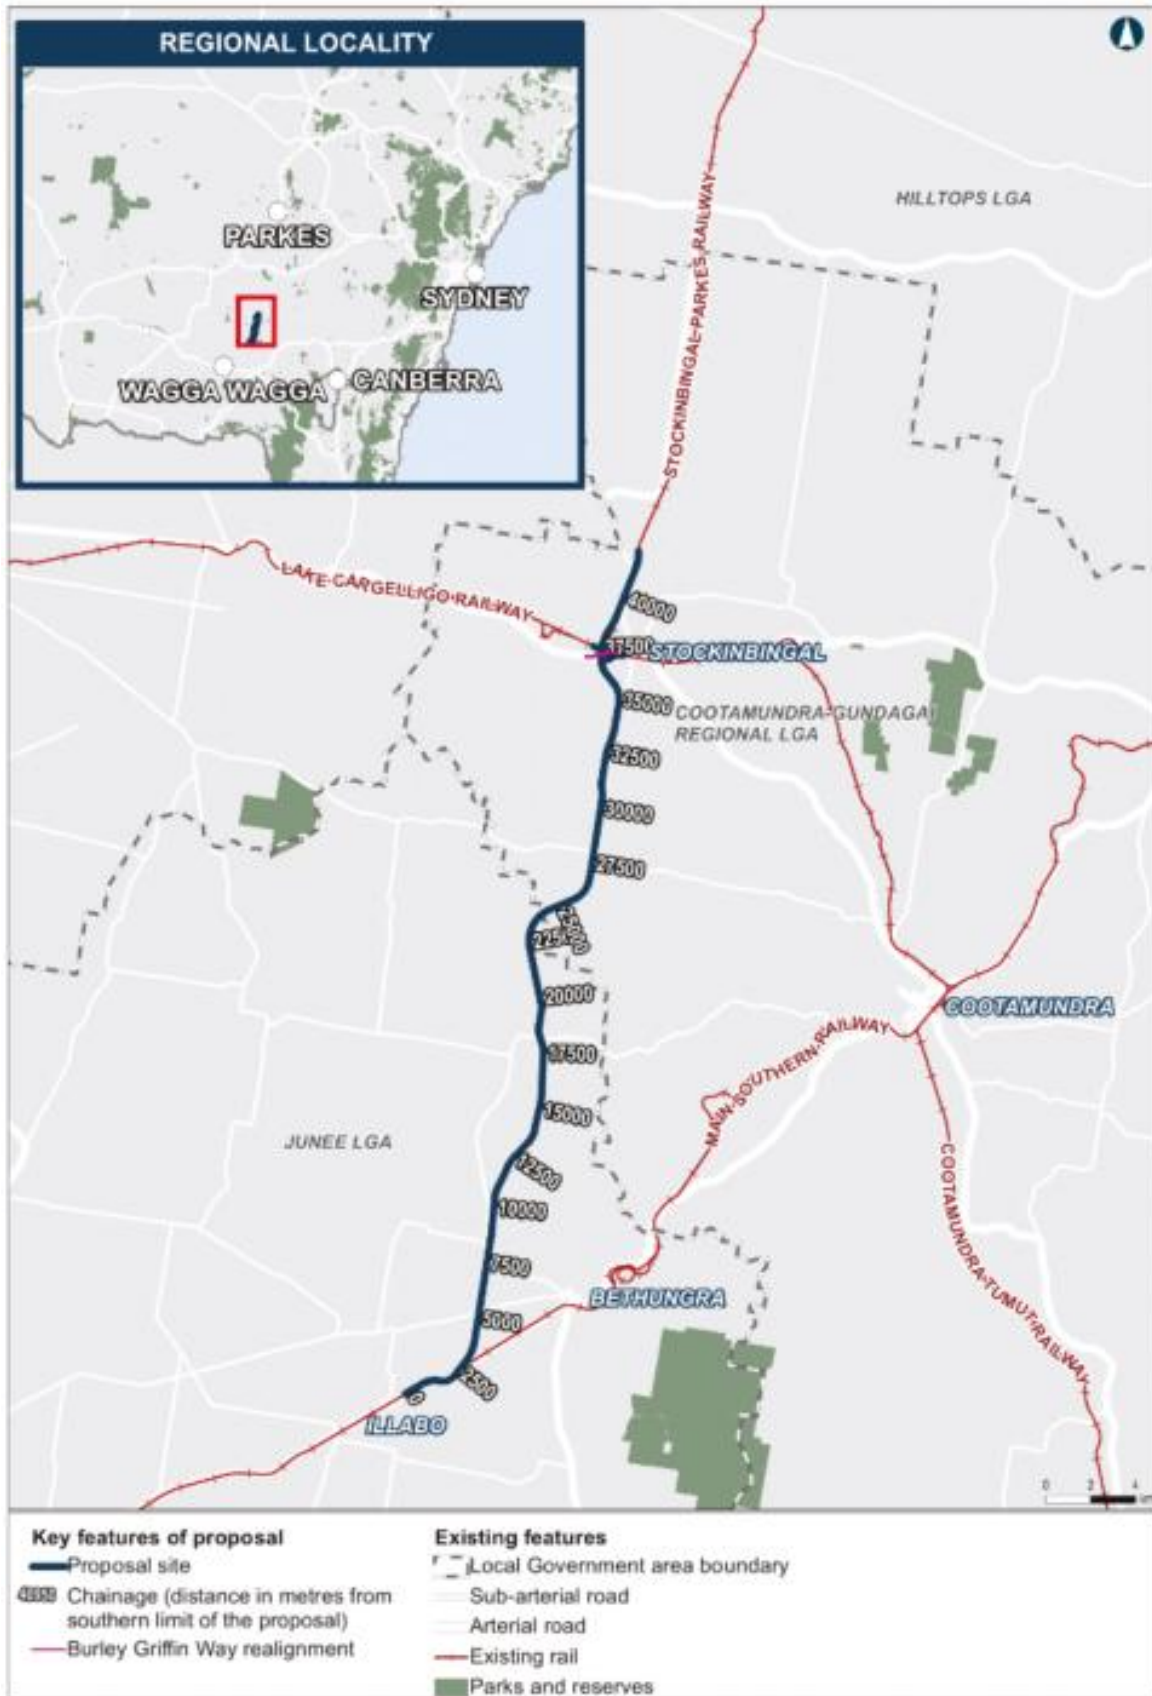


Figure 1-1 Project locality (Source: Illabo to Stockinbingal - Environmental Impact Statement, 2022)

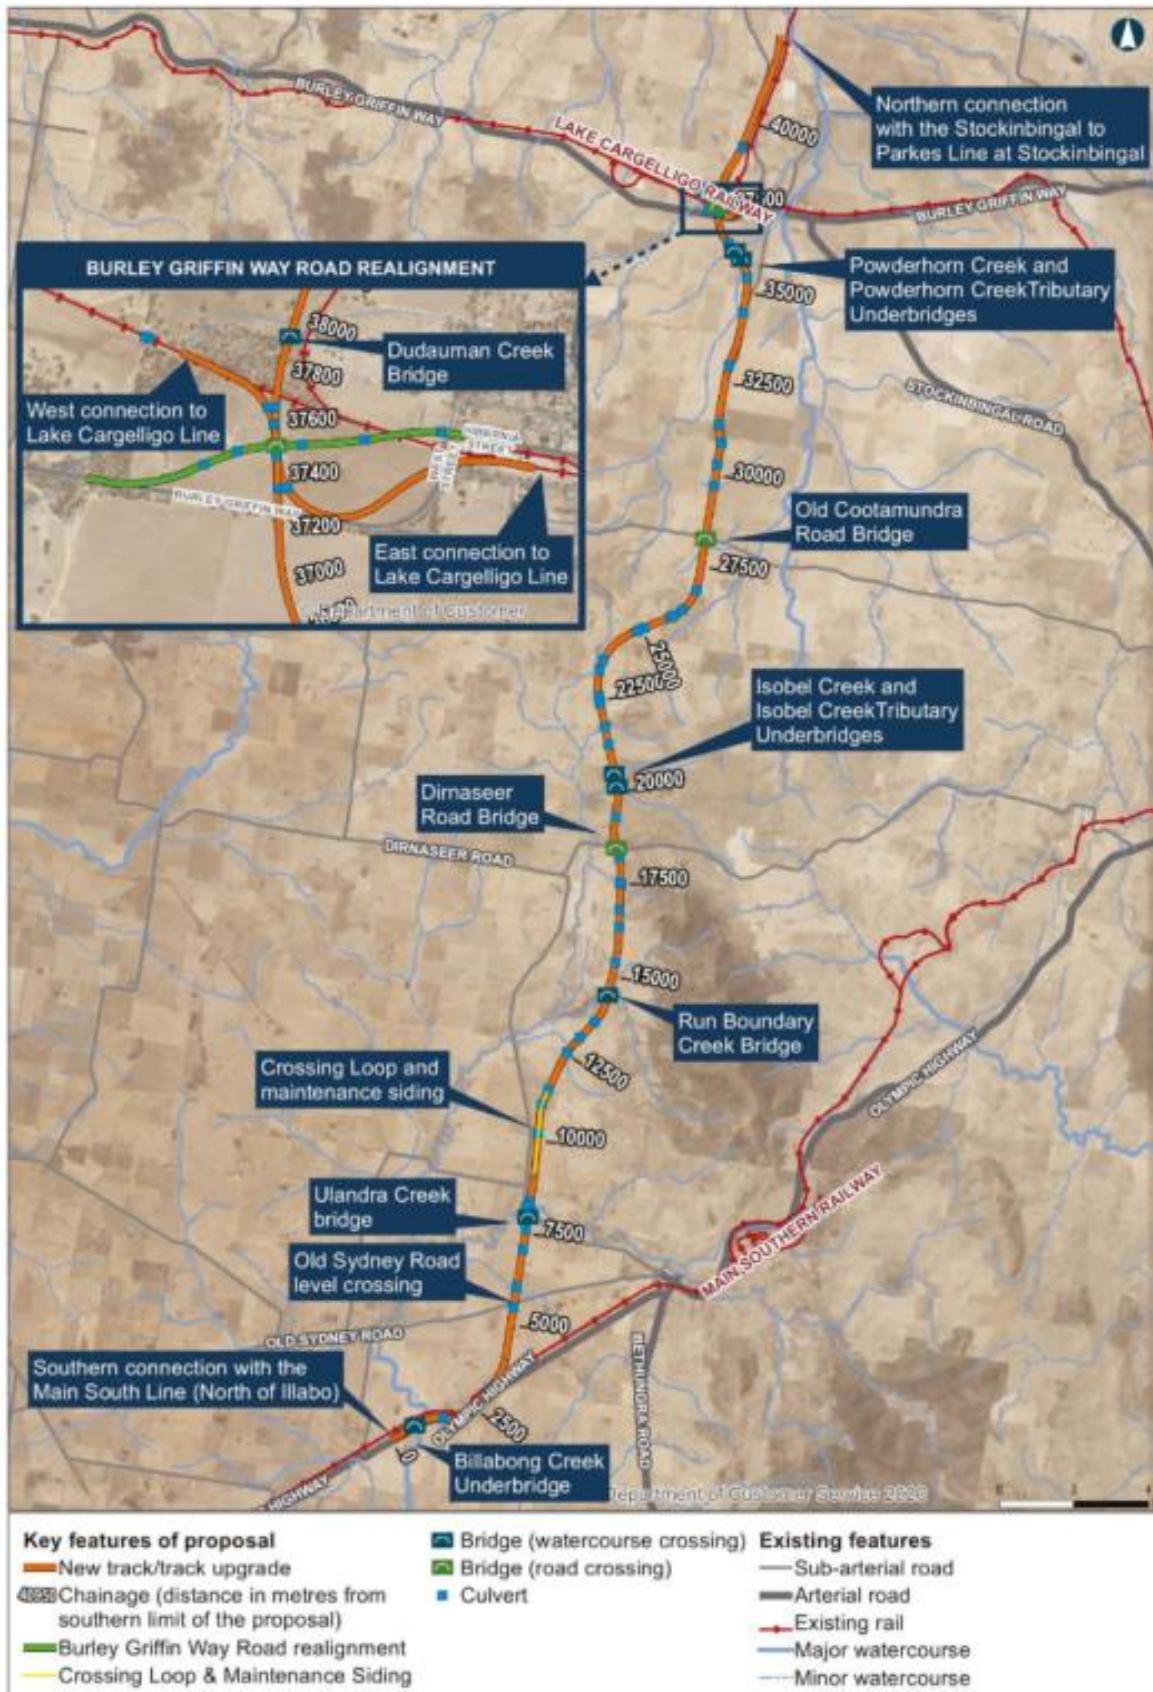


Figure 1-2 Key Project features (Source: Illabo to Stockinbingal - Environmental Impact Statement, 2022)



## 1.2 Report Scope

John Holland Group have been issued an Environment Protection Licence (EPL No. 22021) from NSW Environment Protection Authority (EPA) for Inland Rail – Illabo to Stockinbingal (I2S) Project. The EPL applies to the works approved under the Conditions of Approval for Inland Rail – Illabo to Stockinbingal SSI 9406.

This EPL Monthly Monitoring Report provides the results of all pollution monitoring required to be measured or monitored by the licensee of EPL 22021 as required by Section 66 of the *Protection of the Environment Operations Act 1997* (POEO Act) and with reference to EPA Publication Requirements for publishing pollution monitoring data (Environment Protection Authority, 2013).

Table 2-1 provides a summary of the EPL 22021.

Table 1-1 Details of EPL 22021

|                                              |                                                                                                  |
|----------------------------------------------|--------------------------------------------------------------------------------------------------|
| <b>Name of licensee:</b>                     | JOHN HOLLAND PTY LTD                                                                             |
| <b>ACN</b>                                   | 004 282 268                                                                                      |
| <b>EPL number:</b>                           | 22021                                                                                            |
| <b>Issue date:</b>                           | 26 Aug 2025                                                                                      |
| <b>Premises name and address:</b>            | ILLABO TO STOCKINBINGAL (FUTURE RAIL CORRIDOR IN CONSTRUCTION FOOTPRINT), STOCKINBINGAL NSW 2725 |
| <b>Scheduled activity/activities on EPL:</b> | Railway activities - railway infrastructure construction                                         |

The EPL can be found by following the link to the EPA's website: [EPL 22021](#)

## 1.3 Reporting Requirements

Under the POEO Act, holders of environment protection licences (licensees) must publish or make pollution monitoring data available to members of the public.

The POEO Act Section 66 requires:

“66 Conditions requiring monitoring, certification or provision of information, and related offences

(1) The conditions of a licence may require—

(a) monitoring by the holder of the licence of the activity or work authorised, required or controlled by the licence, including with respect to—

(i) the operation or maintenance of premises or plant, and

(ii) discharges from premises, and

(iii) relevant ambient conditions prevailing on or outside premises, and

(iv) anything required by the conditions of the licence, and

(b) the provision and maintenance of appropriate measuring and recording devices for the purposes of that monitoring, and

(c) the analysis, reporting and retention of monitoring data.

(2) False or misleading information A holder of a licence who supplies information, or on whose behalf information is supplied, to the appropriate regulatory authority under the conditions of the licence is guilty of an offence if the information is false or misleading in a material respect.”

The primary objective of the pollution monitoring reporting requirements is that members of the public have access to the results of all pollution monitoring (which a licence specifies must be carried out) in a way that is meaningful to them. Data for the is presented on a monthly sampling period. Table 2-2 provides a summary of the monitoring requirements of EPL 22021.

Table 1-2 EPL 22021 monitoring requirements

| EPL Condition         | Requirement                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        | Report Reference          |                          |                         |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
|-----------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------|--------------------------|-------------------------|----------------------|---|-----------------------|-----------------------|-----------------------|---|-----------------------|-----------------------|-----------------------|---|-----------------------|-----------------------|-----------------------|---|-----------------------|-----------------------|-----------------------|---|-----------------------|-----------------------|-----------------------|---|-----------------------|-----------------------|-----------------------|---|-----------------------|-----------------------|-----------------------|---|-----------------------|-----------------------|-----------------------|---|-----------------------|-----------------------|-----------------------|----|-----------------------|-----------------------|-----------------------|----|-----------------------|-----------------------|-----------------------|------------|
| Premise maps          |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |                           |                          |                         |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
| A2.3                  | The most recently approved premises map(s) must be available for public viewing on the licensee's project website or a related website approved in writing by the EPA no more than 5 business days after the approval of the map(s) by the EPA. The requirements outlined in this condition only come into force when works or activities commence at the licensed premises.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | Appendix A                |                          |                         |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
| Water                 |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |                           |                          |                         |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
| L2.1-L2.4<br><br>M2.2 | <p>Must not exceed limits for oil &amp; grease (≤10), pH (6.5–8.5), TSS (≤50 mg/L), turbidity (≤40.95 NTU) at all monitoring points (1–19).</p> <p>For the purposes of the above water monitoring requirements 'Special Frequency 1' means: Sampling must be undertaken once within 24 hours following the commencement of a controlled discharge event, and then every second day throughout the discharge event when it is safe to do so.</p>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | Section 2.2               |                          |                         |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
| P1.1                  | <p>Must monitor pollutant concentrations at all specified discharge/monitoring points. The following points referred to in the table are identified in this licence for the purpose of the monitoring and/or setting of limits for discharges of pollutants to water from the point.</p> <table><tr><th>EPA Identification Number</th><th>Type of Monitoring Point</th><th>Type of Discharge Point</th><th>Location Description</th></tr><tr><td>1</td><td>Surface Water Quality</td><td>Surface Water Quality</td><td>Discharge point SS-01</td></tr><tr><td>2</td><td>Surface Water Quality</td><td>Surface Water Quality</td><td>Discharge point SS-02</td></tr><tr><td>3</td><td>Surface Water Quality</td><td>Surface Water Quality</td><td>Discharge point SS-03</td></tr><tr><td>4</td><td>Surface Water Quality</td><td>Surface Water Quality</td><td>Discharge point SS-04</td></tr><tr><td>5</td><td>Surface Water Quality</td><td>Surface Water Quality</td><td>Discharge point SS-05</td></tr><tr><td>6</td><td>Surface Water Quality</td><td>Surface Water Quality</td><td>Discharge point SS-06</td></tr><tr><td>7</td><td>Surface Water Quality</td><td>Surface Water Quality</td><td>Discharge point SS-07</td></tr><tr><td>8</td><td>Surface Water Quality</td><td>Surface Water Quality</td><td>Discharge point SB-01</td></tr><tr><td>9</td><td>Surface Water Quality</td><td>Surface Water Quality</td><td>Discharge point SS-08</td></tr><tr><td>10</td><td>Surface Water Quality</td><td>Surface Water Quality</td><td>Discharge point SS-09</td></tr><tr><td>11</td><td>Surface Water Quality</td><td>Surface Water Quality</td><td>Discharge point SS-10</td></tr></table> | EPA Identification Number | Type of Monitoring Point | Type of Discharge Point | Location Description | 1 | Surface Water Quality | Surface Water Quality | Discharge point SS-01 | 2 | Surface Water Quality | Surface Water Quality | Discharge point SS-02 | 3 | Surface Water Quality | Surface Water Quality | Discharge point SS-03 | 4 | Surface Water Quality | Surface Water Quality | Discharge point SS-04 | 5 | Surface Water Quality | Surface Water Quality | Discharge point SS-05 | 6 | Surface Water Quality | Surface Water Quality | Discharge point SS-06 | 7 | Surface Water Quality | Surface Water Quality | Discharge point SS-07 | 8 | Surface Water Quality | Surface Water Quality | Discharge point SB-01 | 9 | Surface Water Quality | Surface Water Quality | Discharge point SS-08 | 10 | Surface Water Quality | Surface Water Quality | Discharge point SS-09 | 11 | Surface Water Quality | Surface Water Quality | Discharge point SS-10 | Appendix B |
|                       | EPA Identification Number                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          | Type of Monitoring Point  | Type of Discharge Point  | Location Description    |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
|                       | 1                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Surface Water Quality     | Surface Water Quality    | Discharge point SS-01   |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
|                       | 2                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Surface Water Quality     | Surface Water Quality    | Discharge point SS-02   |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
|                       | 3                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Surface Water Quality     | Surface Water Quality    | Discharge point SS-03   |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
|                       | 4                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Surface Water Quality     | Surface Water Quality    | Discharge point SS-04   |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
|                       | 5                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Surface Water Quality     | Surface Water Quality    | Discharge point SS-05   |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
|                       | 6                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Surface Water Quality     | Surface Water Quality    | Discharge point SS-06   |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
|                       | 7                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Surface Water Quality     | Surface Water Quality    | Discharge point SS-07   |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
|                       | 8                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Surface Water Quality     | Surface Water Quality    | Discharge point SB-01   |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
|                       | 9                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Surface Water Quality     | Surface Water Quality    | Discharge point SS-08   |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
|                       | 10                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 | Surface Water Quality     | Surface Water Quality    | Discharge point SS-09   |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |
| 11                    | Surface Water Quality                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              | Surface Water Quality     | Discharge point SS-10    |                         |                      |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |   |                       |                       |                       |    |                       |                       |                       |    |                       |                       |                       |            |

|                      |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |                       |                       |                       |             |
|----------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------|-----------------------|-----------------------|-------------|
|                      | 12                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | Surface Water Quality | Surface Water Quality | Discharge point SS-11 |             |
|                      | 13                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | Surface Water Quality | Surface Water Quality | Discharge point WDP-1 |             |
|                      | 14                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | Surface Water Quality | Surface Water Quality | Discharge point WDP-2 |             |
|                      | 15                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | Surface Water Quality | Surface Water Quality | Discharge point WDP-3 |             |
|                      | 16                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | Surface Water Quality | Surface Water Quality | Discharge point WDP-4 |             |
|                      | 17                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | Surface Water Quality | Surface Water Quality | Discharge point WDP-5 |             |
|                      | 18                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | Surface Water Quality | Surface Water Quality | Discharge point WDP-6 |             |
|                      | 19                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | Surface Water Quality | Surface Water Quality | Discharge point WDP-7 |             |
|                      | Note:<br>SS -Farm dam or sediment sump<br>SB- Sediment basin<br>WDP-Waterway                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             |                       |                       |                       |             |
| Weather              |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |                       |                       |                       |             |
| M5.1                 | The licensee must monitor and record temperature, humidity, wind direction, wind velocity and rainfall at either the project weather station, or through analysis of equivalent weather information obtained from the Australian Bureau of Meteorology. Monitoring must:<br>a) be representative of each catchment;<br>b) be undertaken prior to any works that may cause sediment to leave the premises; and<br>c) continue to be operated until soil disturbance activities cease at the premises and the site has been stabilised.                                                                    |                       |                       |                       | Section 2.1 |
| Noise                |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |                       |                       |                       |             |
| L6.7                 | Despite Condition L6.1, work may be undertaken during the hours of 6:00 am to 6:00 pm each day provided:<br>a) no work affects any given receiver between the hours of 6:00 pm on a Saturday and 7:00 am on a Monday every second week;<br>b) only low impact noise activities (defined in Condition L5.3) are permitted between 6.00 am and 7.00 am; and<br>c) consultation with affected receivers occurs at least every three months, or more frequently following complaints recorded in the Complaints Register required by Condition M4.1, to determine respite or additional mitigation measures. |                       |                       |                       | Section 2.3 |
| L4                   | Airblast Overpressure must not exceed: <ul style="list-style-type: none"><li>120 dB (lin peak) at any residence or sensitive receiver, at any time.</li><li>115 dB (lin peak) at any receiver for more than 5% of blasts over the project.</li></ul> Blasting hours are restricted to: <ul style="list-style-type: none"><li>9:00 am – 5:00 pm Monday–Friday</li><li>9:00 am – 1:00 pm Saturdays</li><li>No blasting on Sundays or public holidays</li></ul> Exceptions require EPA written approval                                                                                                     |                       |                       |                       | Section 2.4 |
| Pollution complaints |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |                       |                       |                       |             |
| M6.1                 | The licensee must keep a legible record of all complaints made to the licensee or any employee or agent of the licensee in relation to pollution arising from any activity to which this licence applies.                                                                                                                                                                                                                                                                                                                                                                                                |                       |                       |                       | Section 2.5 |



|      |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   |             |
|------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|
| M6.2 | <p>The record must include details of the following:</p> <ul style="list-style-type: none"><li>a) the date and time of the complaint;</li><li>b) the method by which the complaint was made;</li><li>c) any personal details of the complainant which were provided by the complainant or, if no such details were provided, a note to that effect;</li><li>d) the nature of the complaint;</li><li>e) the action taken by the licensee in relation to the complaint, including any follow-up contact with the complainant; and</li><li>f) if no action was taken by the licensee, the reasons why no action was taken.</li></ul> | Section 2.5 |
|------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|

## 2 Monitoring

This section presents summaries of the monitoring completed in the reporting period from 1 June 2026 to 30 June 2026.

### 2.1 Weather

Local weather stations and site weather stations (rain gauges) were utilised for weather data across the Project, including:

- Stockinbinal weather station (Sunnydale), station number 073150,
- Junee Treatment Works weather station, station number 073019,
- Cootamundra Airport, station number 073142.

Parameters monitored included temperature, rainfall, relative humidity, wind speed and wind direction, in accordance with EPL Condition M5.1. A summary of daily weather observations (BoM station number 073142) for June 2026 is provided in Table 3-1.

Table 2-1 Weather Monitoring Data

| Date | Temperature  |              | Rainfall | Relative Humidity (%) | Wind direction | Wind Speed (km/h) |
|------|--------------|--------------|----------|-----------------------|----------------|-------------------|
|      | Minimum (°C) | Maximum (°C) |          |                       |                |                   |
| 1    | 4.9          | 14.6         | 0        | 78                    | WNW            | 9                 |
| 2    | 8.7          | 15.2         | 11.4     | 85                    | NNE            | 44                |
| 3    | 8.7          | 13.5         | 10.4     | 87                    | WNW            | 33                |
| 4    | 8.5          | 12.5         | 13.6     | 84                    | WNW            | 33                |
| 5    | 7.8          | 12.4         | 1.4      | 95                    | WSW            | 33                |
| 6    | 0.5          | 14           | 0        | 91                    | WNW            | 9                 |
| 7    | 0.5          | 11           | 0        | 100                   | SSE            | 8                 |
| 8    | 1.9          | 17           | 0        | 100                   | SSW            | 9                 |
| 9    | 2.0          | 18.9         | 0        | 83                    | NNE            | 17                |
| 10   | 8.2          | 16           | 0        | 76                    | NNE            | 33                |
| 11   | 13.4         | 18.9         | 0        | 97                    | NNW            | 4                 |
| 12   | 1.9          | 19.1         | 0        | 100                   | SSW            | 9                 |
| 13   | 2.6          | 17.0         | 0        | 99                    | SSE            | 9                 |
| 14   | 6.8          | 19.4         | 3.4      | 97                    | NNW            | 9                 |
| 15   | 6            | 17.9         | 0        | 95                    | SSE            | 9                 |
| 16   | 3.3          | 19.9         | 0        | 99                    | ENE            | 9                 |
| 17   | 7.8          | 19.5         | 0        | 97                    | ENE            | 4                 |
| 18   | 5.5          | 18.1         | 0        | 100                   | NNW            | 9                 |
| 19   | 10           | 14           | 9.8      | 97                    | ENE            | 4                 |



| Date | Temperature  |              | Rainfall | Relative Humidity (%) | Wind direction | Wind Speed (km/h) |
|------|--------------|--------------|----------|-----------------------|----------------|-------------------|
|      | Minimum (°C) | Maximum (°C) |          |                       |                |                   |
| 20   | 9.9          | 12.9         | 5.4      | 93                    | NNW            | 24                |
| 21   | 8.1          | 12.9         | 0.5      | 95                    | NNW            | 4                 |
| 22   | 5.9          | 14           | 0        | 100                   | SSW            | 4                 |
| 23   | 0.7          | 9.1          | 0        | 99                    | SSW            | 4                 |
| 24   | 3.6          | 10           | 0        | 91                    | WSW            | 4                 |
| 25   | 4            | 15.1         | 0        | 100                   | SSE            | 9                 |
| 26   | 4.6          | 14.5         | 0        | 82                    | SSE            | 9                 |
| 27   | 2            | 14.5         | 2        | 100                   |                |                   |
| 28   | 6.9          | 16.1         | 0        | 79                    | SSE            | 17                |
| 29   | 10.1         | 14           | 0        | 90                    | NNW            | 4                 |
| 30   | 10           | 15.4         | 0        | 79                    | NNE            | 33                |



## 2.2 Water

There was 57.9mm of rainfall recorded within the Project area during June 2026. Water quality monitoring results as per condition M2.3 were recorded and are provided in Table 2-2.

Table 2-2 Water Quality Monitoring Data

| Discharge Point Number | Date       | Water Quality Monitoring Result |                 |            |
|------------------------|------------|---------------------------------|-----------------|------------|
|                        |            | pH                              | Turbidity (NTU) | Oil/Grease |
| SB-01                  | 16/06/2026 | 6.50                            | 39.70           | No         |
| SB-01                  | 17/06/2026 | 6.54                            | 37.30           | No         |
| SS-06                  | 23/06/2026 | 6.85                            | 38.30           | No         |
| SS-06                  | 24/06/2026 | 6.55                            | 39.10           | No         |
| SS-06                  | 25/06/2026 | 6.72                            | 35.10           | No         |
| SS-08                  | 25/06/2026 | 7.92                            | 40.45           | No         |
| SS-06                  | 26/06/2026 | 6.69                            | 39.92           | No         |
| SS-06                  | 27/06/2026 | 6.82                            | 40.2            | No         |

## 2.3 Noise

Noise monitoring is required to validate noise predictions for work undertaken outside of standard construction hours in accordance with the construction noise and vibration assessment and monitoring plan. All noise monitoring performed under EPL are included in Table 3-2.

Table 2-3 Noise Monitoring Data

| Date    | Time  | Monitoring Location              | Attended / Continuous | Construction Activity | NML (dBA) | Predicted (dBA) | Recorded LAeq(15min) (dBA) | LAmx | LAmn | LA10 | Exceedance of Predicted (dBA) | Comments                                                                                                                                                                   |
|---------|-------|----------------------------------|-----------------------|-----------------------|-----------|-----------------|----------------------------|------|------|------|-------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 14 June | 11:00 | 555 Ironbong Road, Bethungra     | Attended              | Bulk earthworks       | 40        | 43.9            | 51.3                       | 75.5 | 34.5 | 54.2 | +7.4                          | Compliant – exceedance attributable to non-project related noise including traffic on Ironbong Rd and birds.                                                               |
| 14 June | 11:30 | 693 Ironbong Road, Bethungra     | Attended              | Bulk earthworks       | 40        | 45.4            | 52.7                       | 78.7 | 23.4 | 55.6 | +7.3                          | Compliant – exceedance attributable to non-project related noise including traffic on Ironbong Rd, horses, and birds.                                                      |
| 14 June | 12:10 | 852 Ironbong Road, Bethungra     | Attended              | Bulk earthworks       | 40        | 46.8            | 43.6                       | 68.6 | 20.7 | 49.7 | +3.6                          | Compliant – exceedance attributable to non-project related noise including traffic on Ironbong Rd and birds.                                                               |
| 14 June | 13:00 | 128 Dudauman Road, Stockinbingal | Attended              | Bulk earthworks       | 40        | 45              | 62.5                       | 91.6 | 23.9 | 49   | +22.5                         | Compliant – exceedance attributable to non-project related noise including traffic on Dudauman Rd (multiple light and heavy trucks). Construction noise sometimes audible. |

Revision No: 1

Issue Date: 08/07/2026

IRPL Document Number: 6-0019-220-PES-00-RP-0001

When printed this document is an uncontrolled version and must be checked against the Aconex electronic version for validity

| Date    | Time  | Monitoring Location               | Attended / Continuous | Construction Activity                | NML (dBA) | Predicted (dBA) | Recorded LAeq(15min) (dBA) | LAmx | LAmn | LA10 | Exceedance of Predicted (dBA) | Comments                                                                                                                                                                                |
|---------|-------|-----------------------------------|-----------------------|--------------------------------------|-----------|-----------------|----------------------------|------|------|------|-------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 17 June | 19:00 | Burley Griffin Way, Stockinbingal | Attended              | Utility (watermain) relocation works | 35        | <NML            | 67.1                       | 90.4 | 27.6 | 60.1 | +32.1                         | Compliant – exceedance attributable to non-project related noise including very frequent heavy and light vehicle movements on Burley Griffin Way. Construction noise sometimes audible. |
| 17 June | 20:22 | 2 West St, Stockinbingal          | Attended              | Utility (watermain) relocation works | 35        | <NML            | 54.6                       | 71.8 | 36.6 | 55.4 | +19.6                         | Compliant – exceedance attributable to non-project related noise including very frequent heavy and light vehicle movements on Burley Griffin Way. Construction noise sometimes audible. |
| 17 June | 23:27 | 71 Troy St, Stockinbingal         | Attended              | Utility (watermain) relocation works | 35        | <NML            | 47                         | 66.6 | 27.8 | 45.9 | +12                           | Compliant – exceedance attributable to non-project related noise including very frequent heavy and light vehicle movements on Burley Griffin Way. Construction noise sometimes audible. |
| 21 June | 09:45 | 1673 Dimnaseer Rd, Bethungra      | Attended              | Bulk earthworks, bridge construction | 40        | 46.7            | 52.1                       | 79.8 | 29.6 | 46.3 | +5.4                          | Compliant – exceedance attributable to non-project related noise including traffic on                                                                                                   |

Revision No: 1

Issue Date: 08/07/2026

IRPL Document Number: 6-0019-220-PES-00-RP-0001

When printed this document is an uncontrolled version and must be checked against the Aconex electronic version for validity

| Date    | Time  | Monitoring Location          | Attended / Continuous | Construction Activity | NML (dBA) | Predicted (dBA) | Recorded LAeq(15min) (dBA) | LAmx | LAmn | LA10 | Exceedance of Predicted (dBA) | Comments                                                                                                                                                                                                       |
|---------|-------|------------------------------|-----------------------|-----------------------|-----------|-----------------|----------------------------|------|------|------|-------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|         |       |                              |                       |                       |           |                 |                            |      |      |      |                               | Dirnaseer Rd and birds.                                                                                                                                                                                        |
| 21 June | 10:24 | 555 Ironbong Rd, Bethungra   | Attended              | Drainage construction | 40        | 49.2            | 57.3                       | 88.4 | 23.1 | 50.4 | +8.1                          | Compliant – exceedance attributable to non-project related noise including traffic on Dirnaseer Rd (including a honk).                                                                                         |
| 26 June | 11:55 | 1673 Dirnaseer Rd, Bethungra | Attended              | Blasting              | 40        | N/A             | 54                         | 80.1 | 36.8 | 50.8 | N/A                           | Compliant – exceedance attributable to sounding siren prior to blasting and the blast itself, with an impact duration of <1 minute. Other sources of noise included bird activity and traffic on Dirnaseer Rd. |
| 28 June | 14:35 | Walbridge Ln, Illabo         | Attended              | Bulk earthworks       | 40        | 57.2            | 52.8                       | 72.6 | 37.2 | 55.8 | -4.4                          | Compliant – exceedance attributable to non-project related noise including heavy vehicle traffic on Olympic Highway.                                                                                           |

Revision No: 1

Issue Date: 08/07/2026

IRPL Document Number: 6-0019-220-PES-00-RP-0001

When printed this document is an uncontrolled version and must be checked against the Aconex electronic version for validity



2.4 Blasting

Blasting activities were undertaken during the reporting period in the Project area during June 2026. Blast monitoring results as per condition L4.1 and L4.2 and vibration monitoring were recorded and are provided in Table 2-4.

Table 2-4 Blast Monitoring Data

| Cut 19 | 200m from blast                       |                               | 300m from blast                       |                               | At nearest receiver(s)*               |                               |
|--------|---------------------------------------|-------------------------------|---------------------------------------|-------------------------------|---------------------------------------|-------------------------------|
|        | Peak Vector<br>Sum Velocity<br>[mm/s] | Peak<br>Overpressure<br>(dBL) | Peak Vector<br>Sum Velocity<br>[mm/s] | Peak<br>Overpressure<br>(dBL) | Peak Vector<br>Sum Velocity<br>[mm/s] | Peak<br>Overpressure<br>(dBL) |
|        | 5.59                                  | 74.1                          | 3.13                                  | 80.9                          | Did not<br>trigger                    | Did not<br>trigger            |

Notes:\* A blast monitor was set up at the nearest receiver for the purpose of recording ground vibration and air overpressure. Trigger levels were set to 0.26mm/s and 108dBL.

## 2.5 Pollution Complaints

No pollution complaints were received during the reporting period (June 2026). The complaints register indicates that four complaints were recorded across all weeks within the month. The project complaints management system, including the community complaints line and notification procedures, remained in place and operational in accordance with EPL Conditions M6 and M7. Investigations, responses, and corrective actions in response to complaints received are provided in Table 2-5.

Table 2-5 Complaints

| #                                                    | Date received | Time received/initiated | Method received | #  | Avoidable/Unavoidable | Chainage/suburb | Complaint/enquiry/feedback       | Nature of complaint | Number of people affected in relation to a complaint | Details of complaint                                                                                                                                                                                                        | Initial response to complaint (if no action taken, reason(s) why)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              | Further action taken (if required) after the initial response and resolution                                                        | Means by which the complaint was addressed (e.g. email, call, meeting) | Procedure/timeframe                                                                                                                                                                                                                                                                                                                                                                           | Mediation required (Y/N) | Status of complaint |
|------------------------------------------------------|---------------|-------------------------|-----------------|----|-----------------------|-----------------|----------------------------------|---------------------|------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------|---------------------|
| Week concluding 5 June 2026 - 2 complaints received  |               |                         |                 |    |                       |                 |                                  |                     |                                                      |                                                                                                                                                                                                                             |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                                                                                                                                     |                                                                        |                                                                                                                                                                                                                                                                                                                                                                                               |                          |                     |
| 17                                                   | 01-Jun-26     | 13.35                   | Phone call in   | 17 | Avoidable             | Bethungra       | Project staff using private road | Worker behaviour    | 1                                                    | Two project vehicles were observed travelling along the landowner's private road. The road is an unapproved access road.                                                                                                    | EB thanked CF for reaching out, and confirmed that all staff are communicated that this is an unapproved project access road. EB reassured CF that they would investigate the details and communicate again to all staff through internal email and pre starts. EB apologised that this had occurred. EB informed CF that further signage would also be placed on the road to avoid further incidents.                                                                                                                                                                                                                                                                                                                         | Messaging communicated to project staff through internal email and pre start. Additional signage placed on landowners private road. | Project Staff emailed, Phone call, pre starts                          | 13.35 Phone call in to report the complaint<br>13.45 Details of complaint raised with senior staff to investigate drivers.<br>14.05 Email sent to all John Holland Project Staff to remind them that the private road is not to be used<br>15.20 EB closed out complaint with a follow up phone call to CF to inform him of action taken. CF thanked staff for how the complaint was handled. | N                        | Closed              |
| 18                                                   | 03-Jun-26     | 18.3                    | Phone Call In   | 18 | Avoidable             | Stockinbingal   | Project staff driver behaviour   | Worker behaviour    | 1                                                    | Local resident raised concern that a John Holland branded vehicle which appeared to be driving above the speed limit within Stockinbingal township. The driving behaviour caused splashing of water on the horses and cart. | EB thanked stakeholder for bringing this incident to their attention. EB informed the resident/stakeholder that the project is committed to the safety of our community in which we are working. The resident/stakeholder identified the vehicle as a white dual cab with John Holland branding. He was unable to identify the hi vis identification number. EB apologised that the incident occurred and reassured him that his concern would be communicated to all staff at pre start. EB encouraged the resident/stakeholder to reach out again if had any further concerns. The resident/stakeholder thanked EB for listening and taking his concern seriously and confirmed he did not require any additional follow up. | EB communicated with Senior John Holland staff and placed a reminder about driver behaviour in the Daily Bulletin                   | Phone calls daily<br>Pre Start Bulletin 5th June                       | 18.30 3/06/26 Received complaint and spoke with local resident/stakeholder<br>8.00 04/06/26 Spoke with Senior Project staff and actioned Daily Bulletin Pre Start information for 5th June.                                                                                                                                                                                                   | N                        | Closed              |
| Week concluding 12 June 2026 - 0 complaints received |               |                         |                 |    |                       |                 |                                  |                     |                                                      |                                                                                                                                                                                                                             |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                                                                                                                                     |                                                                        |                                                                                                                                                                                                                                                                                                                                                                                               |                          |                     |
|                                                      |               |                         |                 |    |                       |                 |                                  |                     |                                                      |                                                                                                                                                                                                                             |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                                                                                                                                     |                                                                        |                                                                                                                                                                                                                                                                                                                                                                                               |                          |                     |
| Week concluding 19 June 2026 - 0 complaints received |               |                         |                 |    |                       |                 |                                  |                     |                                                      |                                                                                                                                                                                                                             |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                                                                                                                                     |                                                                        |                                                                                                                                                                                                                                                                                                                                                                                               |                          |                     |
|                                                      |               |                         |                 |    |                       |                 |                                  |                     |                                                      |                                                                                                                                                                                                                             |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                                                                                                                                     |                                                                        |                                                                                                                                                                                                                                                                                                                                                                                               |                          |                     |
| Week concluding 26 June 2026 - 2 complaints received |               |                         |                 |    |                       |                 |                                  |                     |                                                      |                                                                                                                                                                                                                             |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                                                                                                                                     |                                                                        |                                                                                                                                                                                                                                                                                                                                                                                               |                          |                     |

| #  | Date received | Time received/initiated | Method received | #  | Avoidable/Unavoidable | Chainage/suburb | Complaint/enquiry/feedback                                            | Nature of complaint | Number of people affected in relation to a complaint | Details of complaint                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 | Initial response to complaint (if no action taken, reason(s) why)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     | Further action taken (if required) after the initial response and resolution                                                    | Means by which the complaint was addressed (e.g. email, call, meeting) | Procedure/timeframe                                                                                                                                                                                                           | Mediation required (Y/N) | Status of complaint |
|----|---------------|-------------------------|-----------------|----|-----------------------|-----------------|-----------------------------------------------------------------------|---------------------|------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------|---------------------|
| 19 | 23-Jun-26     | 16:50                   | SMS In          | 19 | Avoidable             | Stockinbingal   | Asking for project drivers to slow down; particularly on public roads | Worker behaviour    | 1                                                    | A landowner reported that a project truck had driven dangerously while moving sheep, posing risks to livestock, workers, and dogs. The landowner resolved the issue directly with the driver at the time and informed EB. EB thanked the landowner, reassured them that staff are educated on safe practices through daily bulletins, inductions, and pre-starts, and asked if further action was needed. The landowner appreciated EB's response and reassurance that driver behavior is taken seriously and communicated to staff. | EB thanked the landowner for letting her know. EB reassured the landowner that education is provided to all project staff through daily bulletins, inductions, pre starts and tool boxes project wide. EB asked the landowner if there is anything further he would like from this incident. Landowner thanked EB for taking on his information and providing reassurance that driver behaviours is taken seriously and communicated to staff. Communication for driver behaviour including for stock movements to be continued through toolbox talks, daily bulletin and inductions. | As part of normal communication within the project worker driving behaviour is communicated daily through various methods       | Phone call                                                             | Immediately after receiving the SMS                                                                                                                                                                                           | N                        | Resolved            |
| 20 | 24-Jun-26     | 8:45                    | Phone Call In   | 20 | Unavoidable           | Bethungra       | Bus stop safety near project road                                     | Worker behaviour    | 5                                                    | 3 trucks undertaking a delivery for the project were driving (within the approved road speed limit) but appeared to be too fast past the Dudauman Lane school bus stop at 4:10pm yesterday afternoon. One of the trucks beeped their horn. 5 of the stakeholder's grandchildren were getting off at the time of the trucks passing thus causing concerns about their safety.                                                                                                                                                         | EB Thanked stakeholder for reaching out to staff<br><br>EB confirmed to stakeholder that the safety of local residents and staff is a priority<br><br>EB informed stakeholder that this event would be looked into and a follow up would be provided                                                                                                                                                                                                                                                                                                                                  | JH staff met with landowners to observe current situation for the bus stop. JH staff to look into safety measure for this area. | Phone call and on site meeting                                         | 24 Jun 26- received complaint from landowner<br>25 Jun 26 - Organised to meet with landowner on site to properly understand the concern<br>25 Jun 26 - Met with landowner on site to discuss concern and view arrival of bus. | N                        | Ongoing             |



# Appendix A Premise Maps



Legend

- Road Names

Other Boundaries

Chainages
- Cadastre

Chainage (Project, m)

Premise Boundary
- ARTC Kilometrage

JOHN

HOLLAND

INLAND

RAIL

PREMISE BOUNDARY MAPS

Date: 19/01/2026

Author: Tess Anastakis

Approver: Trent Doyle

Data Sources: IRPL, JH

Paper: A3

Rev: A



Legend

- Road Names

Other Boundaries

Chainages
- Cadastral

Chainage (Project, m)
- Premise Boundary
- ARTC Kilometrage

JOHN  
HOLLAND

INLAND  
RAIL

PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend

- Road Names Other Boundaries Chainages
- ARTC Kilometerage
  - Cadastral
  - Chainage (Project, m)
  - Premise Boundary



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A





Legend



- Other Boundaries
  - Cadastre
  - Chainages
    - Chainage (Project, m)
    - Premise Boundary
- ARTC Kilometrage



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
 Author: Tess Anastakis  
 Approver: Trent Doyle  
 Data Sources: IRPL, JH

Paper: A3  
 Rev: A



Legend

- Road Names

Other Boundaries

Chainages
- Cadastre

Chainage (Project, m)
- Premise Boundary

ARTC Kilometerage



PREMISE BOUNDARY MAPS

Date: 19/01/2026

Author: Tess Anastakis

Approver: Trent Doyle

Data Sources: IRPL, JH

Paper: A3

Rev: A



- Legend
- |            |                  |
|------------|------------------|
| Road Names | Other Boundaries |
|            | Cadastral        |
|            | Premise Boundary |

**JOHN HOLLAND**

**INLAND RAIL**

**PREMISE BOUNDARY MAPS**

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A





Legend

- Road Names   Other Boundaries   Chainages
- Cadastral
  - Premise Boundary
  - Chainage (Project, m)



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend

|            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastral        | Chainage (Project, m) |
|            | Premise Boundary |                       |

**PREMISE BOUNDARY MAPS**

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend


|            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastral        | Chainage (Project, m) |
|            | Premise Boundary |                       |



**PREMISE BOUNDARY MAPS**

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A




- Legend
- |            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastre         | Chainage (Project, m) |
|            | Premise Boundary |                       |



**PREMISE BOUNDARY MAPS**

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A

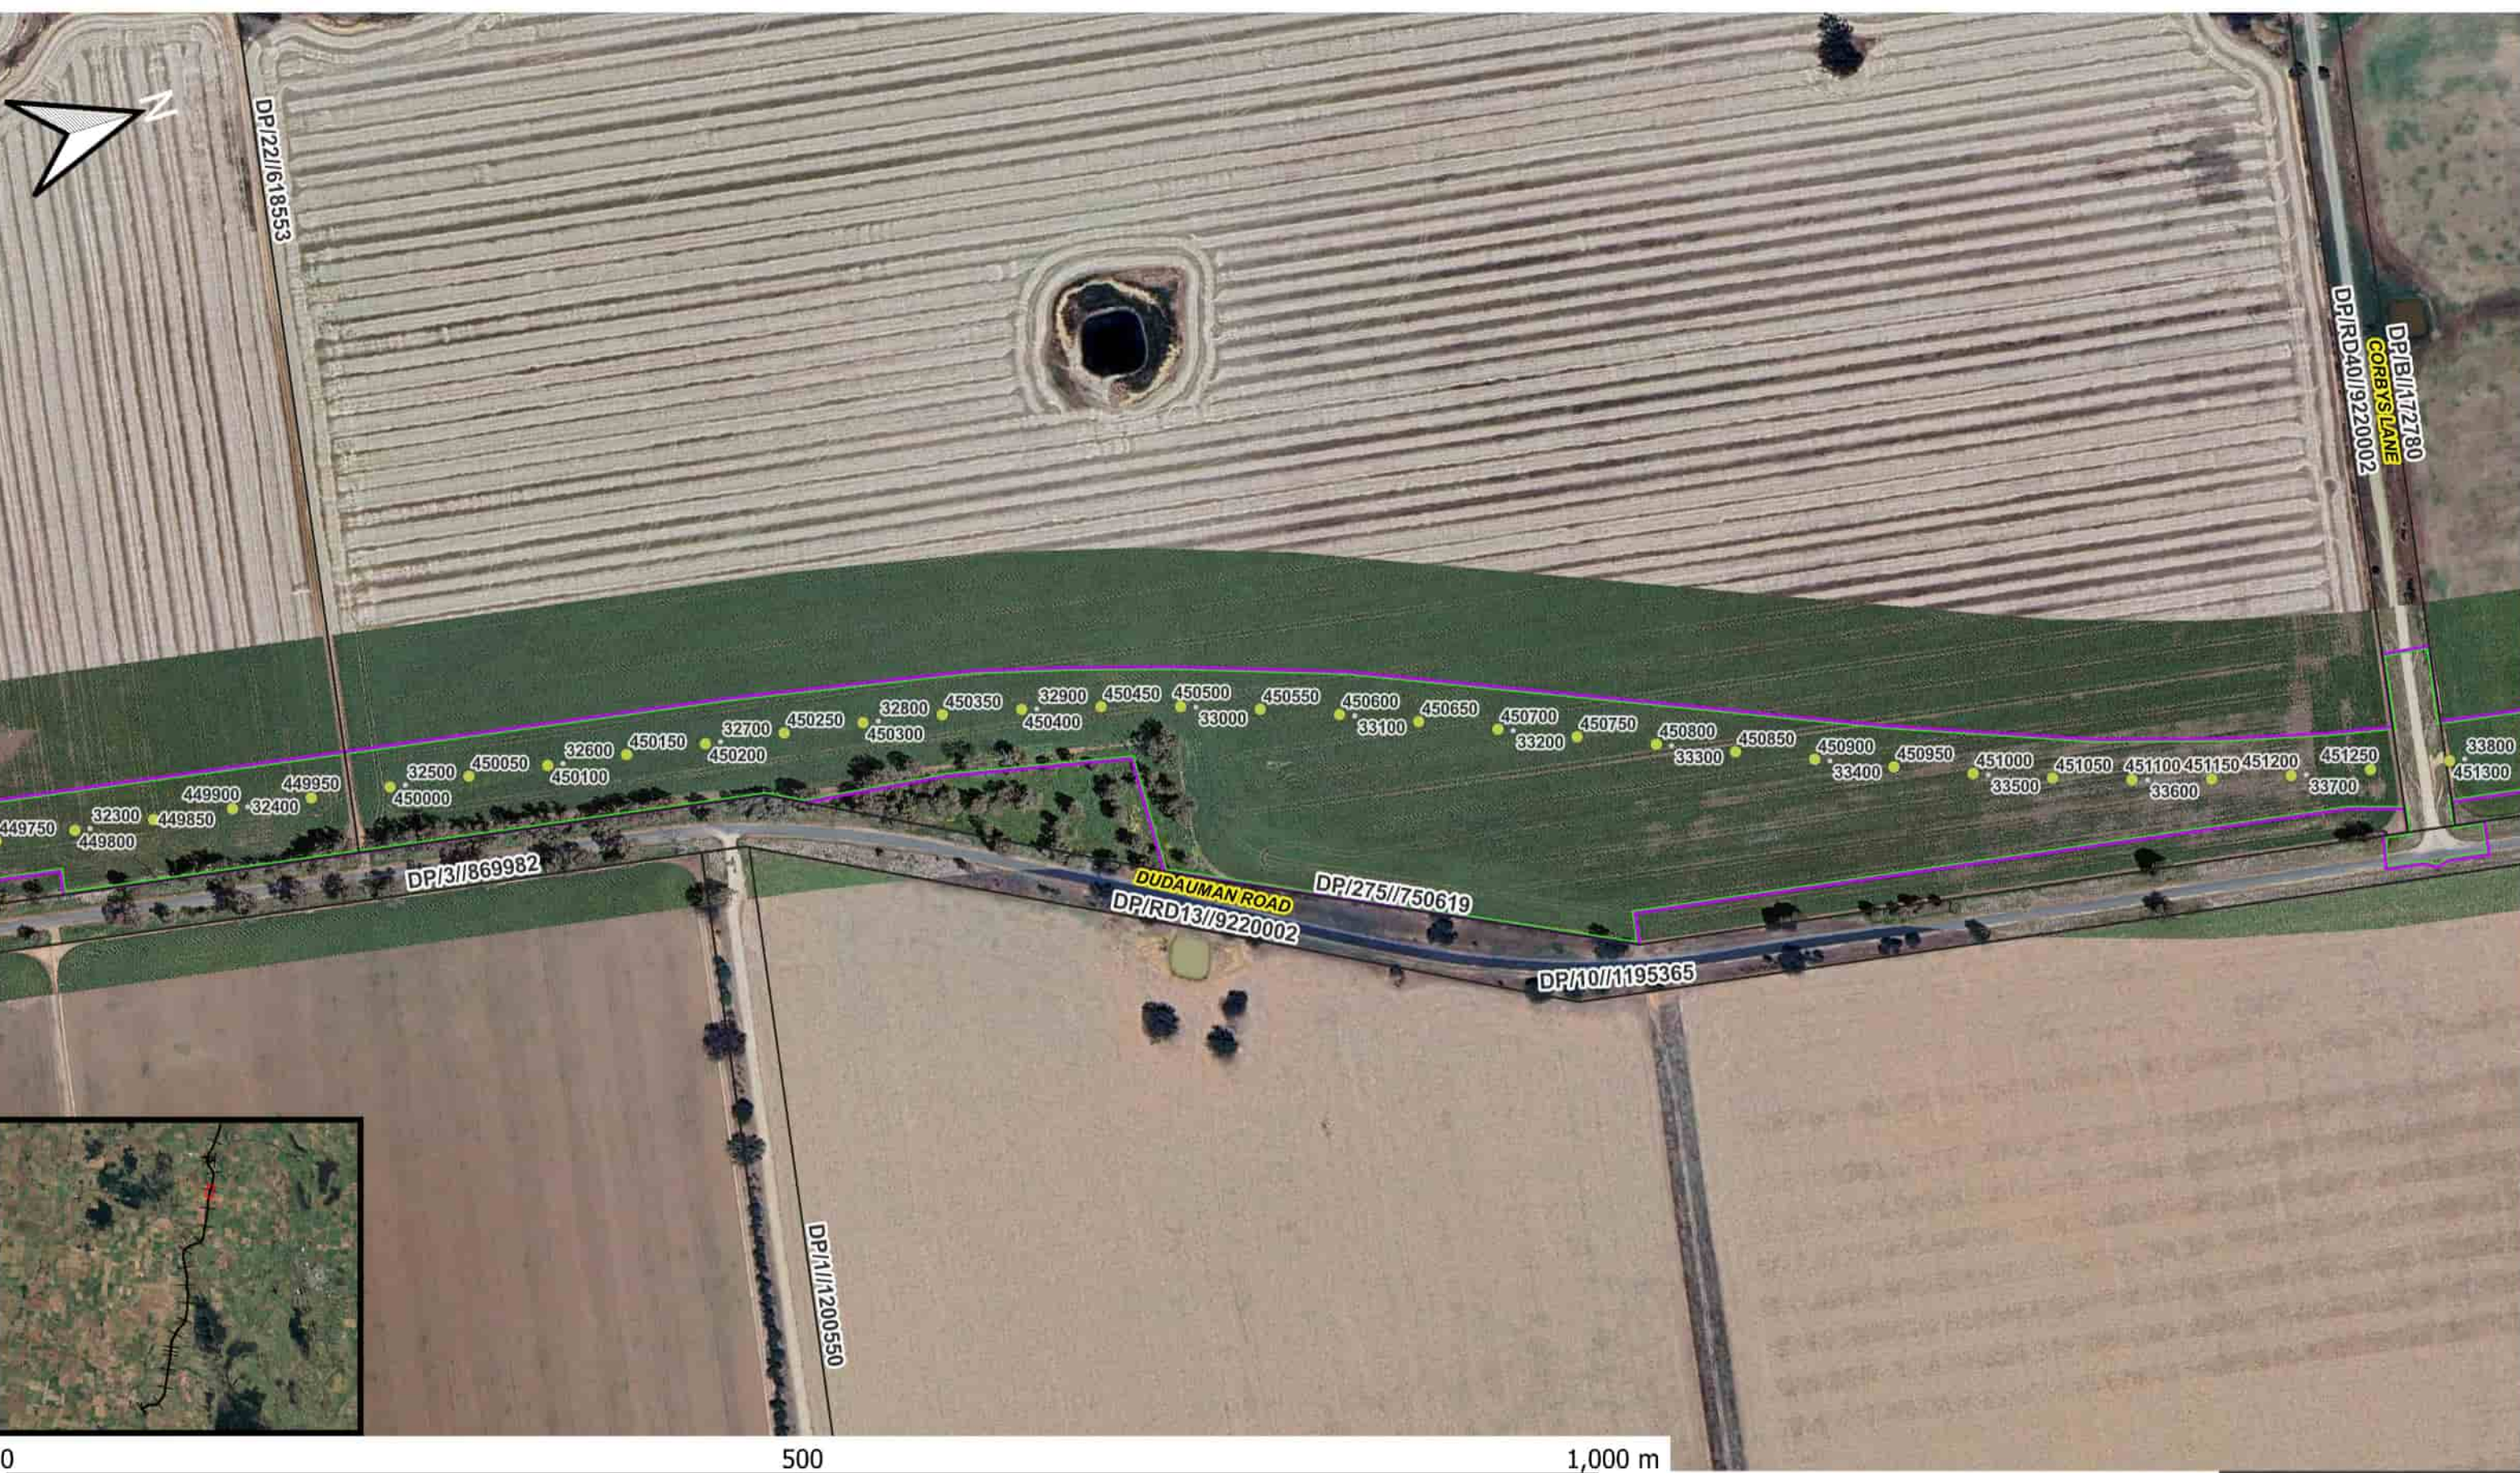

Legend



- Road Names
- Other Boundaries
- Chainages
- Cadastral
- Premise Boundary
- Chainage (Project, m)



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A


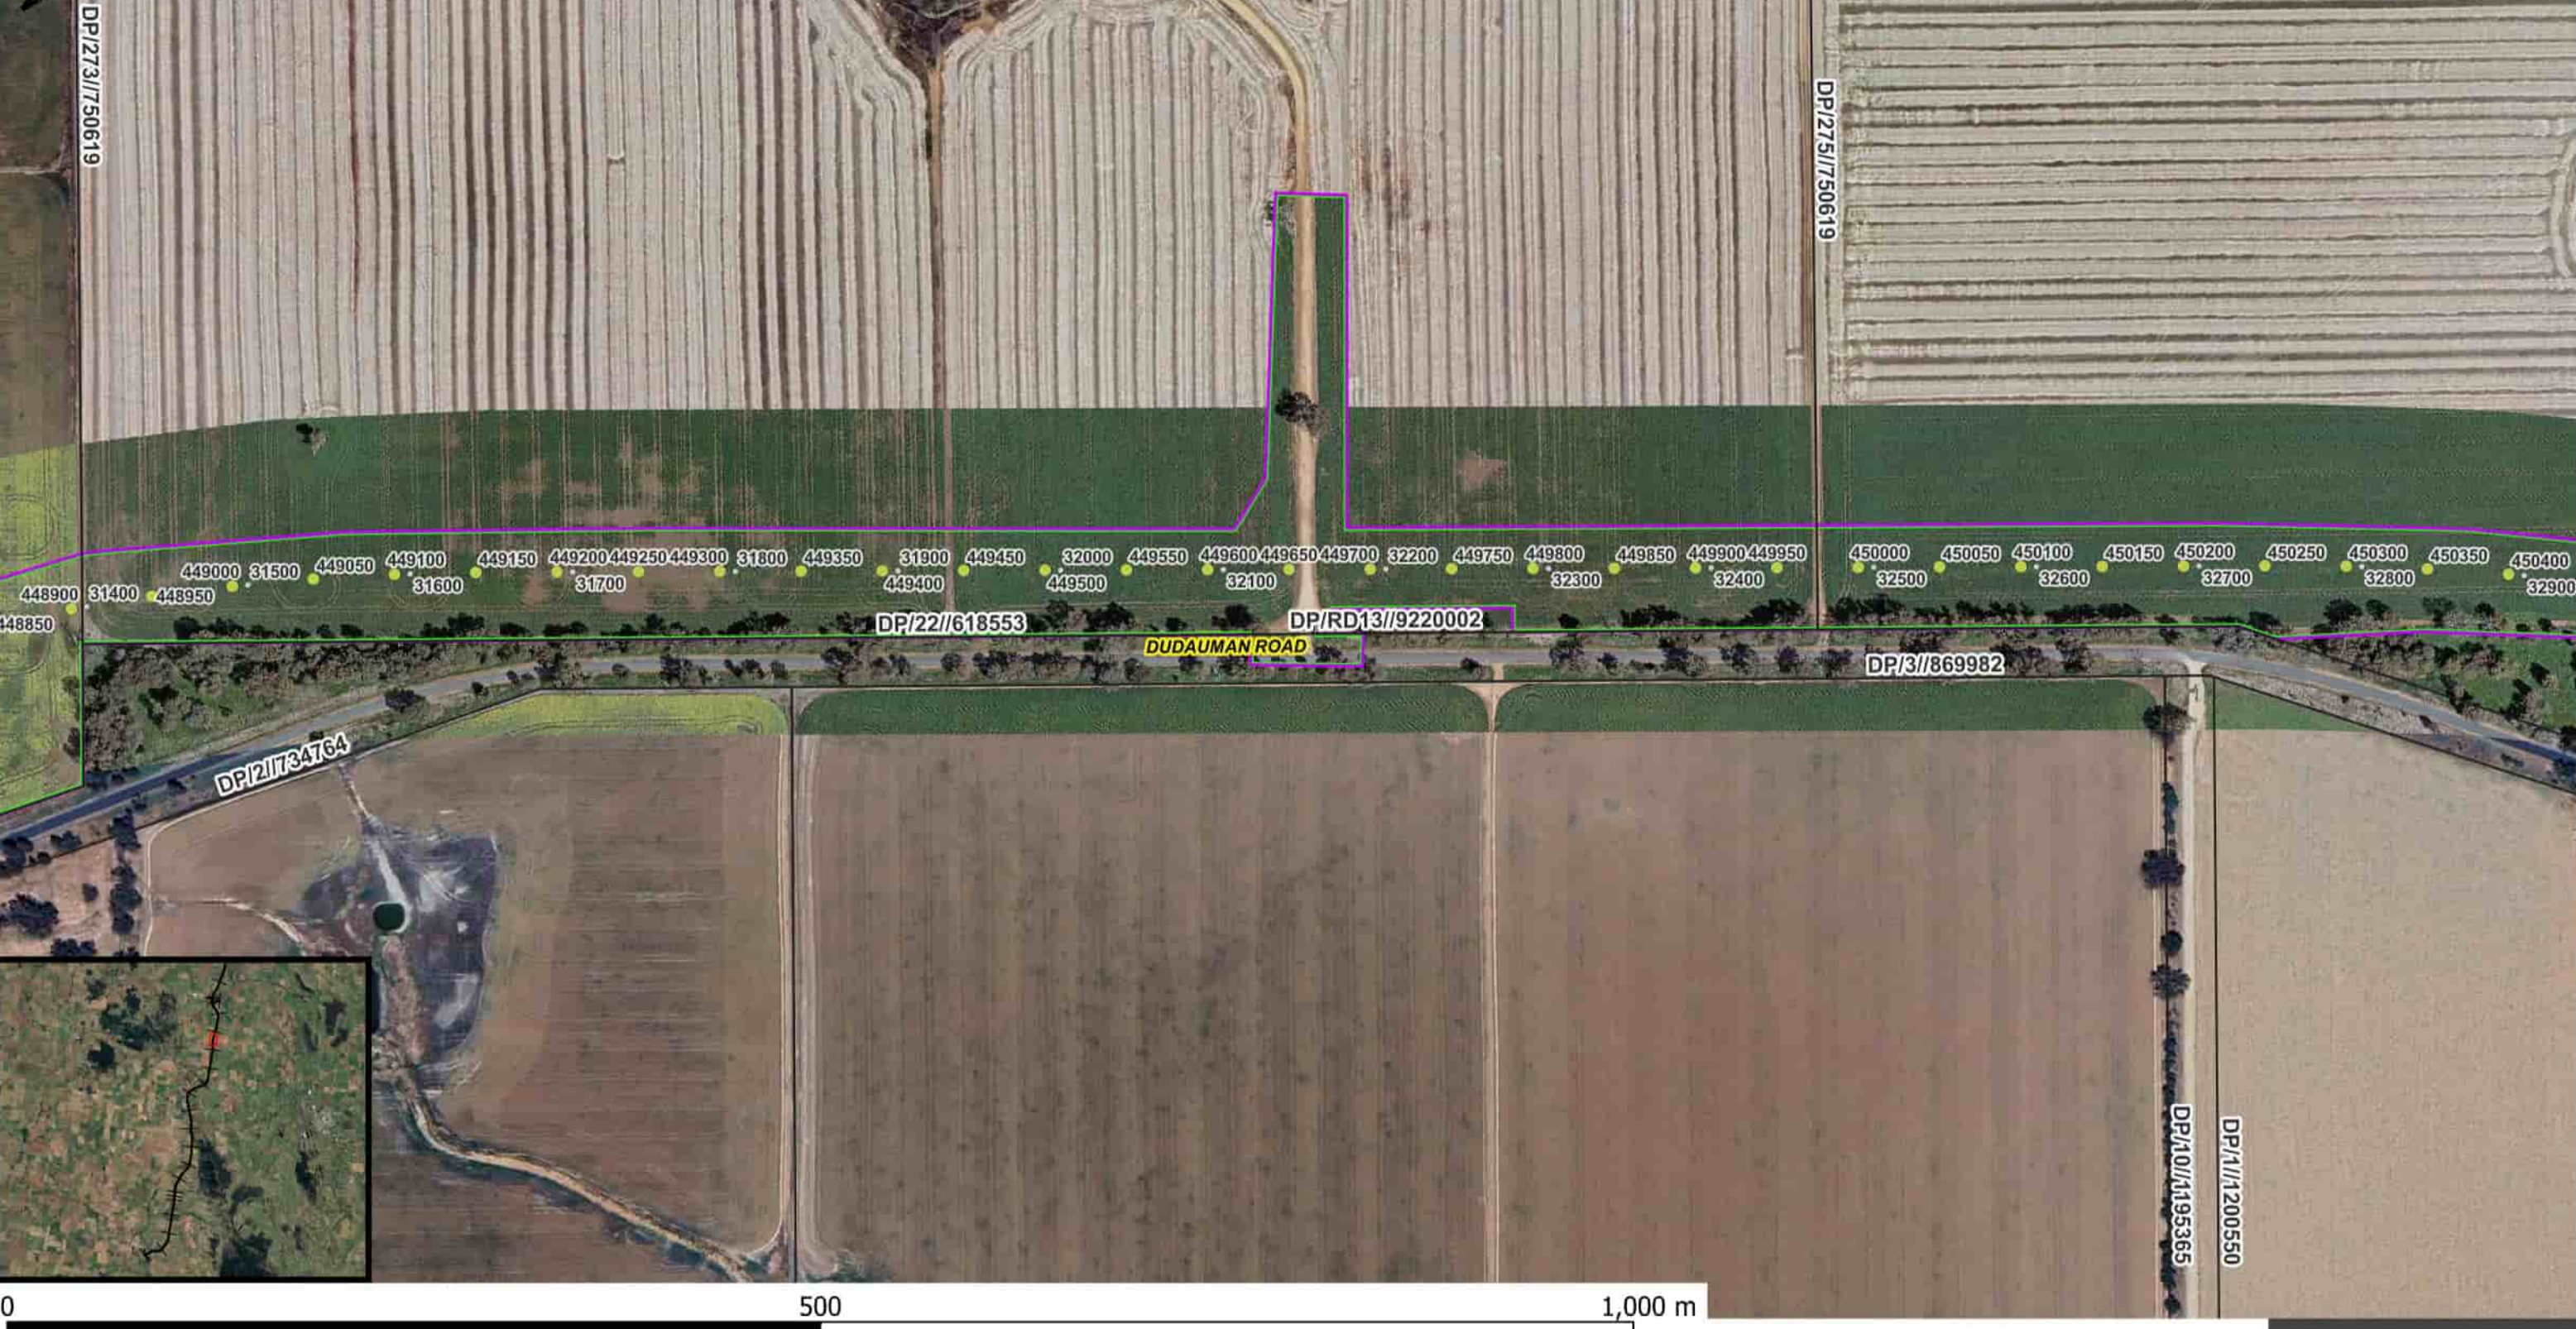


- Legend
- |            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastre         | Chainage (Project, m) |
|            | Premise Boundary |                       |



**PREMISE BOUNDARY MAPS**

|                        |           |
|------------------------|-----------|
| Date: 19/01/2026       | Paper: A3 |
| Author: Tess Anastakis | Rev: A    |
| Approver: Trent Doyle  |           |
| Data Sources: IRPL, JH |           |



- Legend
- |            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastre         | Chainage (Project, m) |
|            | Premise Boundary |                       |



**PREMISE BOUNDARY MAPS**

|                        |           |
|------------------------|-----------|
| Date: 19/01/2026       | Paper: A3 |
| Author: Tess Anastakis | Rev: A    |
| Approver: Trent Doyle  |           |
| Data Sources: IRPL, JH |           |




- Legend
- | Road Names | Other Boundaries | Chainages             |
|------------|------------------|-----------------------|
|            | Cadastre         | Chainage (Project, m) |
|            | Premise Boundary |                       |

PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A

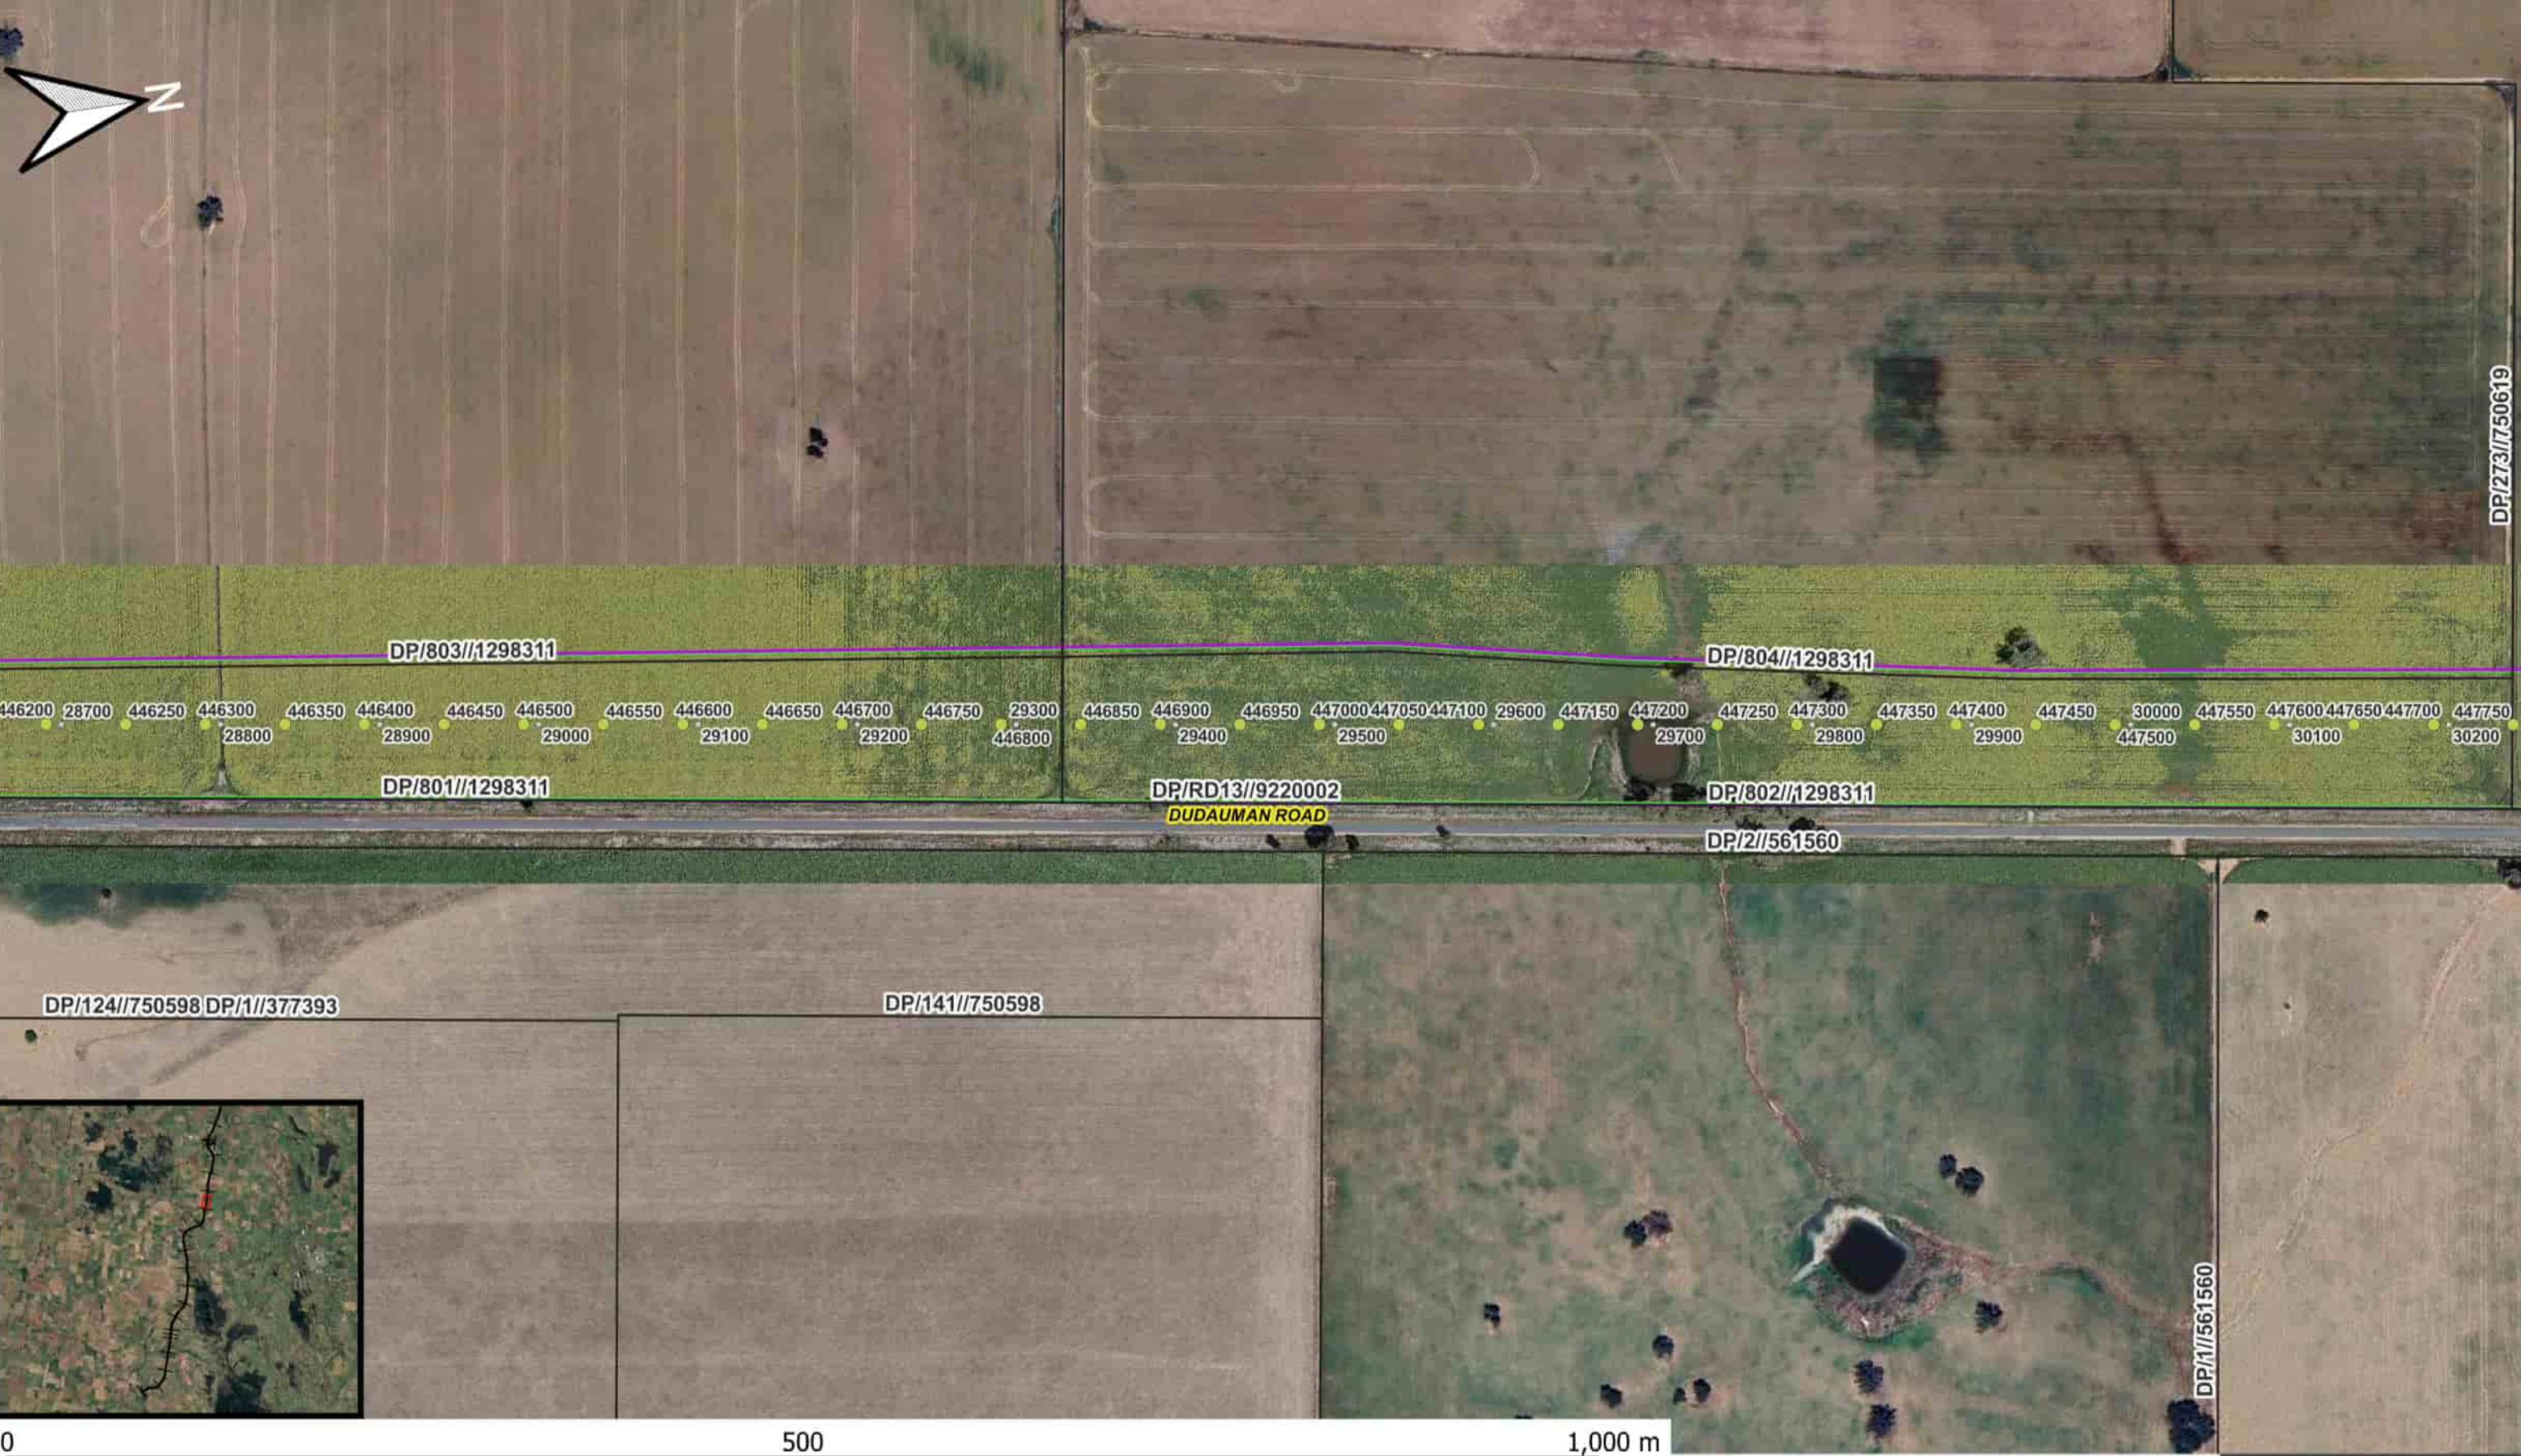

Legend

|            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastral        | Chainage (Project, m) |
|            | Premise Boundary |                       |

**PREMISE BOUNDARY MAPS**

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A







Legend

Other Boundaries   Chainages

Cadastre   Chainage (Project, m)

Premise Boundary

PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



- Legend
- Other Boundaries   Chainages
- Cadastre
  - Chainage (Project, m)
  - Premise Boundary



**PREMISE BOUNDARY MAPS**

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



- Legend
- Other Boundaries   Chainages
- Cadastre
  - Chainage (Project, m)
  - Premise Boundary



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A




- Legend
- Other Boundaries   Chainages
- Cadastre
  - Chainage (Project, m)
  - Premise Boundary



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



- Legend
- Other Boundaries    Chainages
- Cadastre
  - Chainage (Project, m)
  - Premise Boundary



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A






Legend

|            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastral        | Chainage (Project, m) |
|            | Premise Boundary |                       |

PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



DP/16/19/2005

DP/200/1751401

DP/247/1751401

DP/282/1751401  
DP/174/1751401

DP/6/121766  
DP/24/1751401

DP/5/121766

DP/199/1751401  
DP/7/121766

DP/25/1751401

DP/23/1751401

DP/172/1751401

DP/173/1751401  
DP/221/1751401

21200 438700 21100 438600 438650 438550 21000 438500 438450 20900 438400 20800 438300 20700 438200 20600 438100 20500 438000 20400 437800 20200 437700 20100 437600 20000 437500 437450 19900 437350 437300 437250 19700 437200



0 500 1,000 m


- Legend
- Other Boundaries    Chainages
- Cadastre    • Chainage (Project, m)
- Premise Boundary



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



- Legend
- Other Boundaries   Chainages
- Cadastre
  - Chainage (Project, m)
  - Premise Boundary



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend

- Road Names

Other Boundaries

Chainages
- Cadastre

Chainage (Project, m)
- Premise Boundary

JOHN

HOLLAND

INLAND

RAIL

PREMISE BOUNDARY MAPS

Date: 19/01/2026

Author: Tess Anastakis

Approver: Trent Doyle

Data Sources: IRPL, JH

Paper: A3

Rev: A




Legend

|            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastral        | Chainage (Project, m) |
|            | Premise Boundary |                       |

PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend

Other Boundaries   Chainages

Cadastre   Chainage (Project, m)

Premise Boundary

PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend

Other Boundaries    Chainages

Cadastre    • Chainage (Project, m)

Premise Boundary

**JOHN  
HOLLAND**

**INLAND  
RAIL**

**PREMISE BOUNDARY MAPS**

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



- Legend
- Other Boundaries
    - Cadastre
  - Chainages
    - Chainage (Project, m)
    - Premise Boundary

**PREMISE BOUNDARY MAPS**

Date: 19/01/2026  
 Author: Tess Anastakis  
 Approver: Trent Doyle  
 Data Sources: IRPL, JH

Paper: A3  
 Rev: A




- Legend
- Other Boundaries   Chainages
- Cadastre
  - Chainage (Project, m)
  - Premise Boundary

PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



- Legend
- Other Boundaries   Chainages
- Cadastre
  - Chainage (Project, m)
  - Premise Boundary



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



- Legend
- Other Boundaries   Chainages
- Cadastre   • Chainage (Project, m)
- Premise Boundary

**JOHN  
HOLLAND**

**INLAND  
RAIL**

**PREMISE BOUNDARY MAPS**

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend

|            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastral        | Chainage (Project, m) |
|            | Premise Boundary |                       |

**PREMISE BOUNDARY MAPS**

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend

|            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastral        | Chainage (Project, m) |
|            | Premise Boundary |                       |

PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



- Legend
- |            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastral        | Chainage (Project, m) |
|            | Premise Boundary |                       |





PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



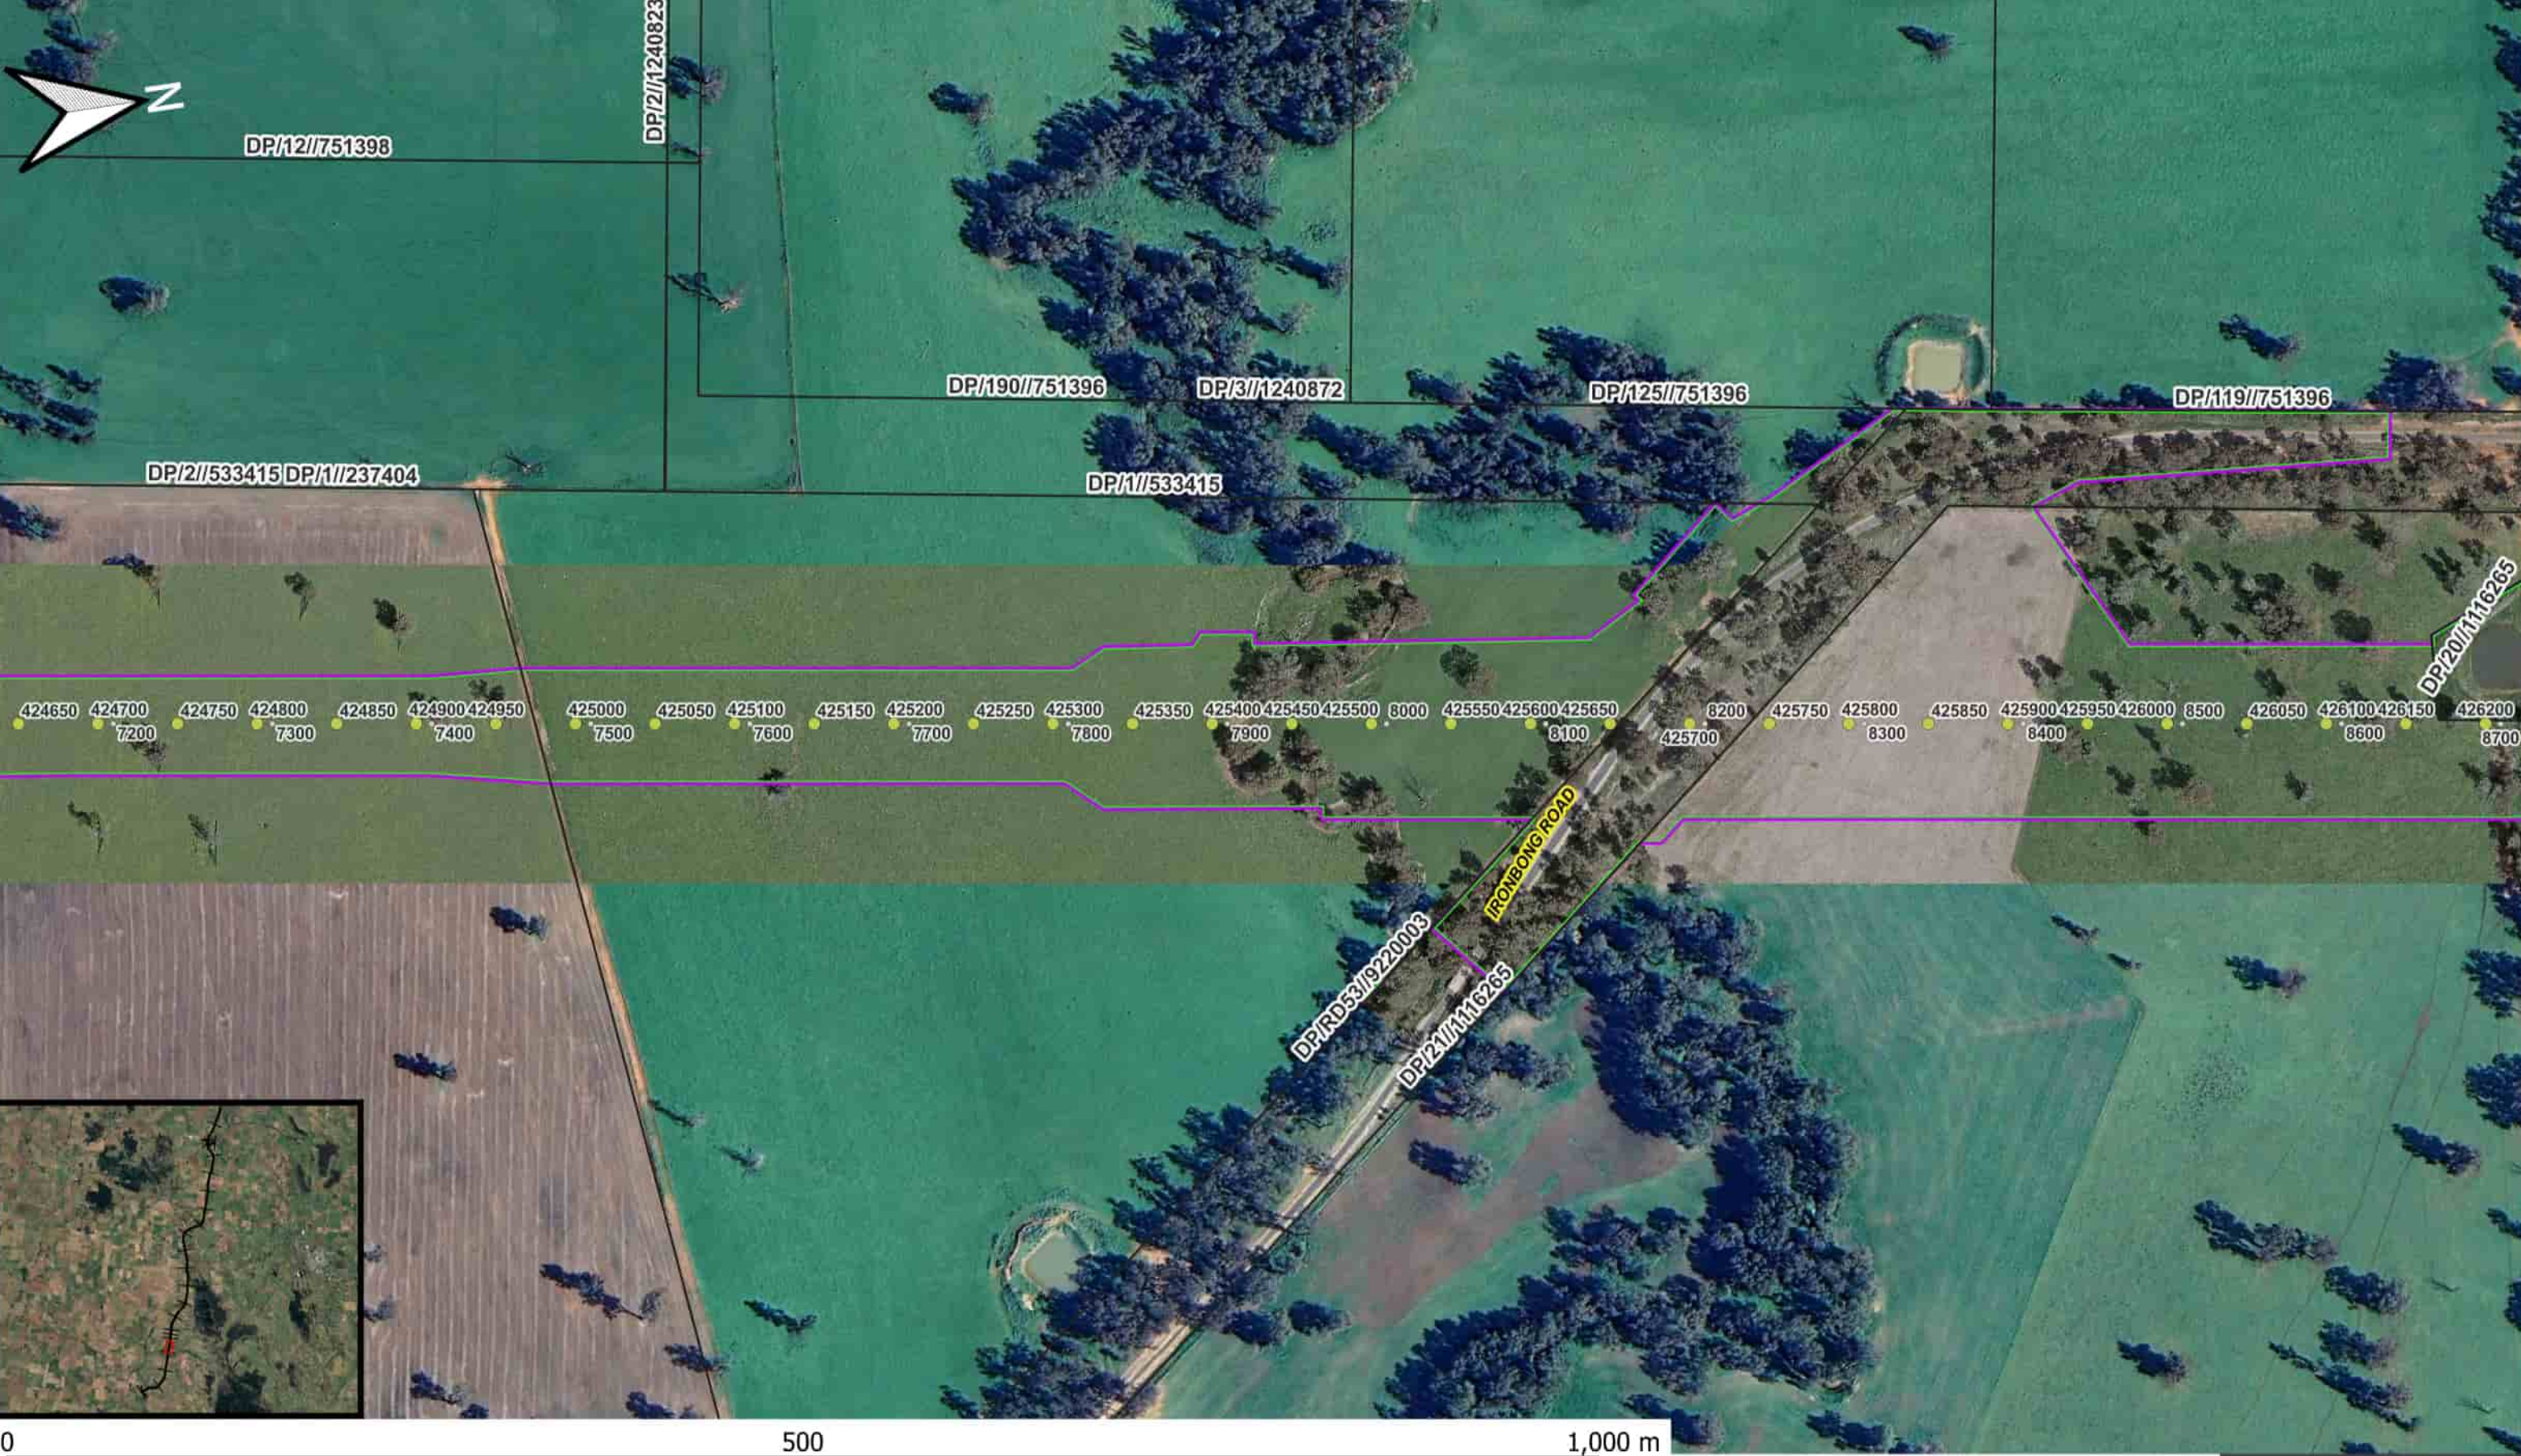

- Legend
- |            |                  |                       |
|------------|------------------|-----------------------|
| Road Names | Other Boundaries | Chainages             |
|            | Cadastral        | Chainage (Project, m) |
|            | Premise Boundary |                       |



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend

| Road Names | Other Boundaries | Chainages             |
|------------|------------------|-----------------------|
|            | Cadastral        | Chainage (Project, m) |
|            | Premise Boundary |                       |

PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend


- Road Names
- Other Boundaries
- Chainages
- Cadastre
- Chainage (Project, m)
- Premise Boundary



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A

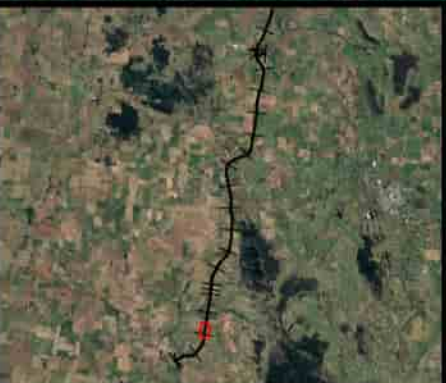


- Legend
- | Road Names | Other Boundaries | Chainages             |
|------------|------------------|-----------------------|
|            | Cadastral        | Chainage (Project, m) |
|            | Premise Boundary |                       |



PREMISE BOUNDARY MAPS

|                        |           |
|------------------------|-----------|
| Date: 19/01/2026       | Paper: A3 |
| Author: Tess Anastakis | Rev: A    |
| Approver: Trent Doyle  |           |
| Data Sources: IRPL, JH |           |



- Legend
- Road Names
  - Other Boundaries
  - Chainages
  - Cadastre
  - Premise Boundary
  - ARTC Kilometrage
  - Chainage (Project, m)



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A





Legend


- Road Names    Other Boundaries    Chainages    ARTC Kilometrage
- Cadastre    Chainage (Project, m)
- Premise Boundary



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A

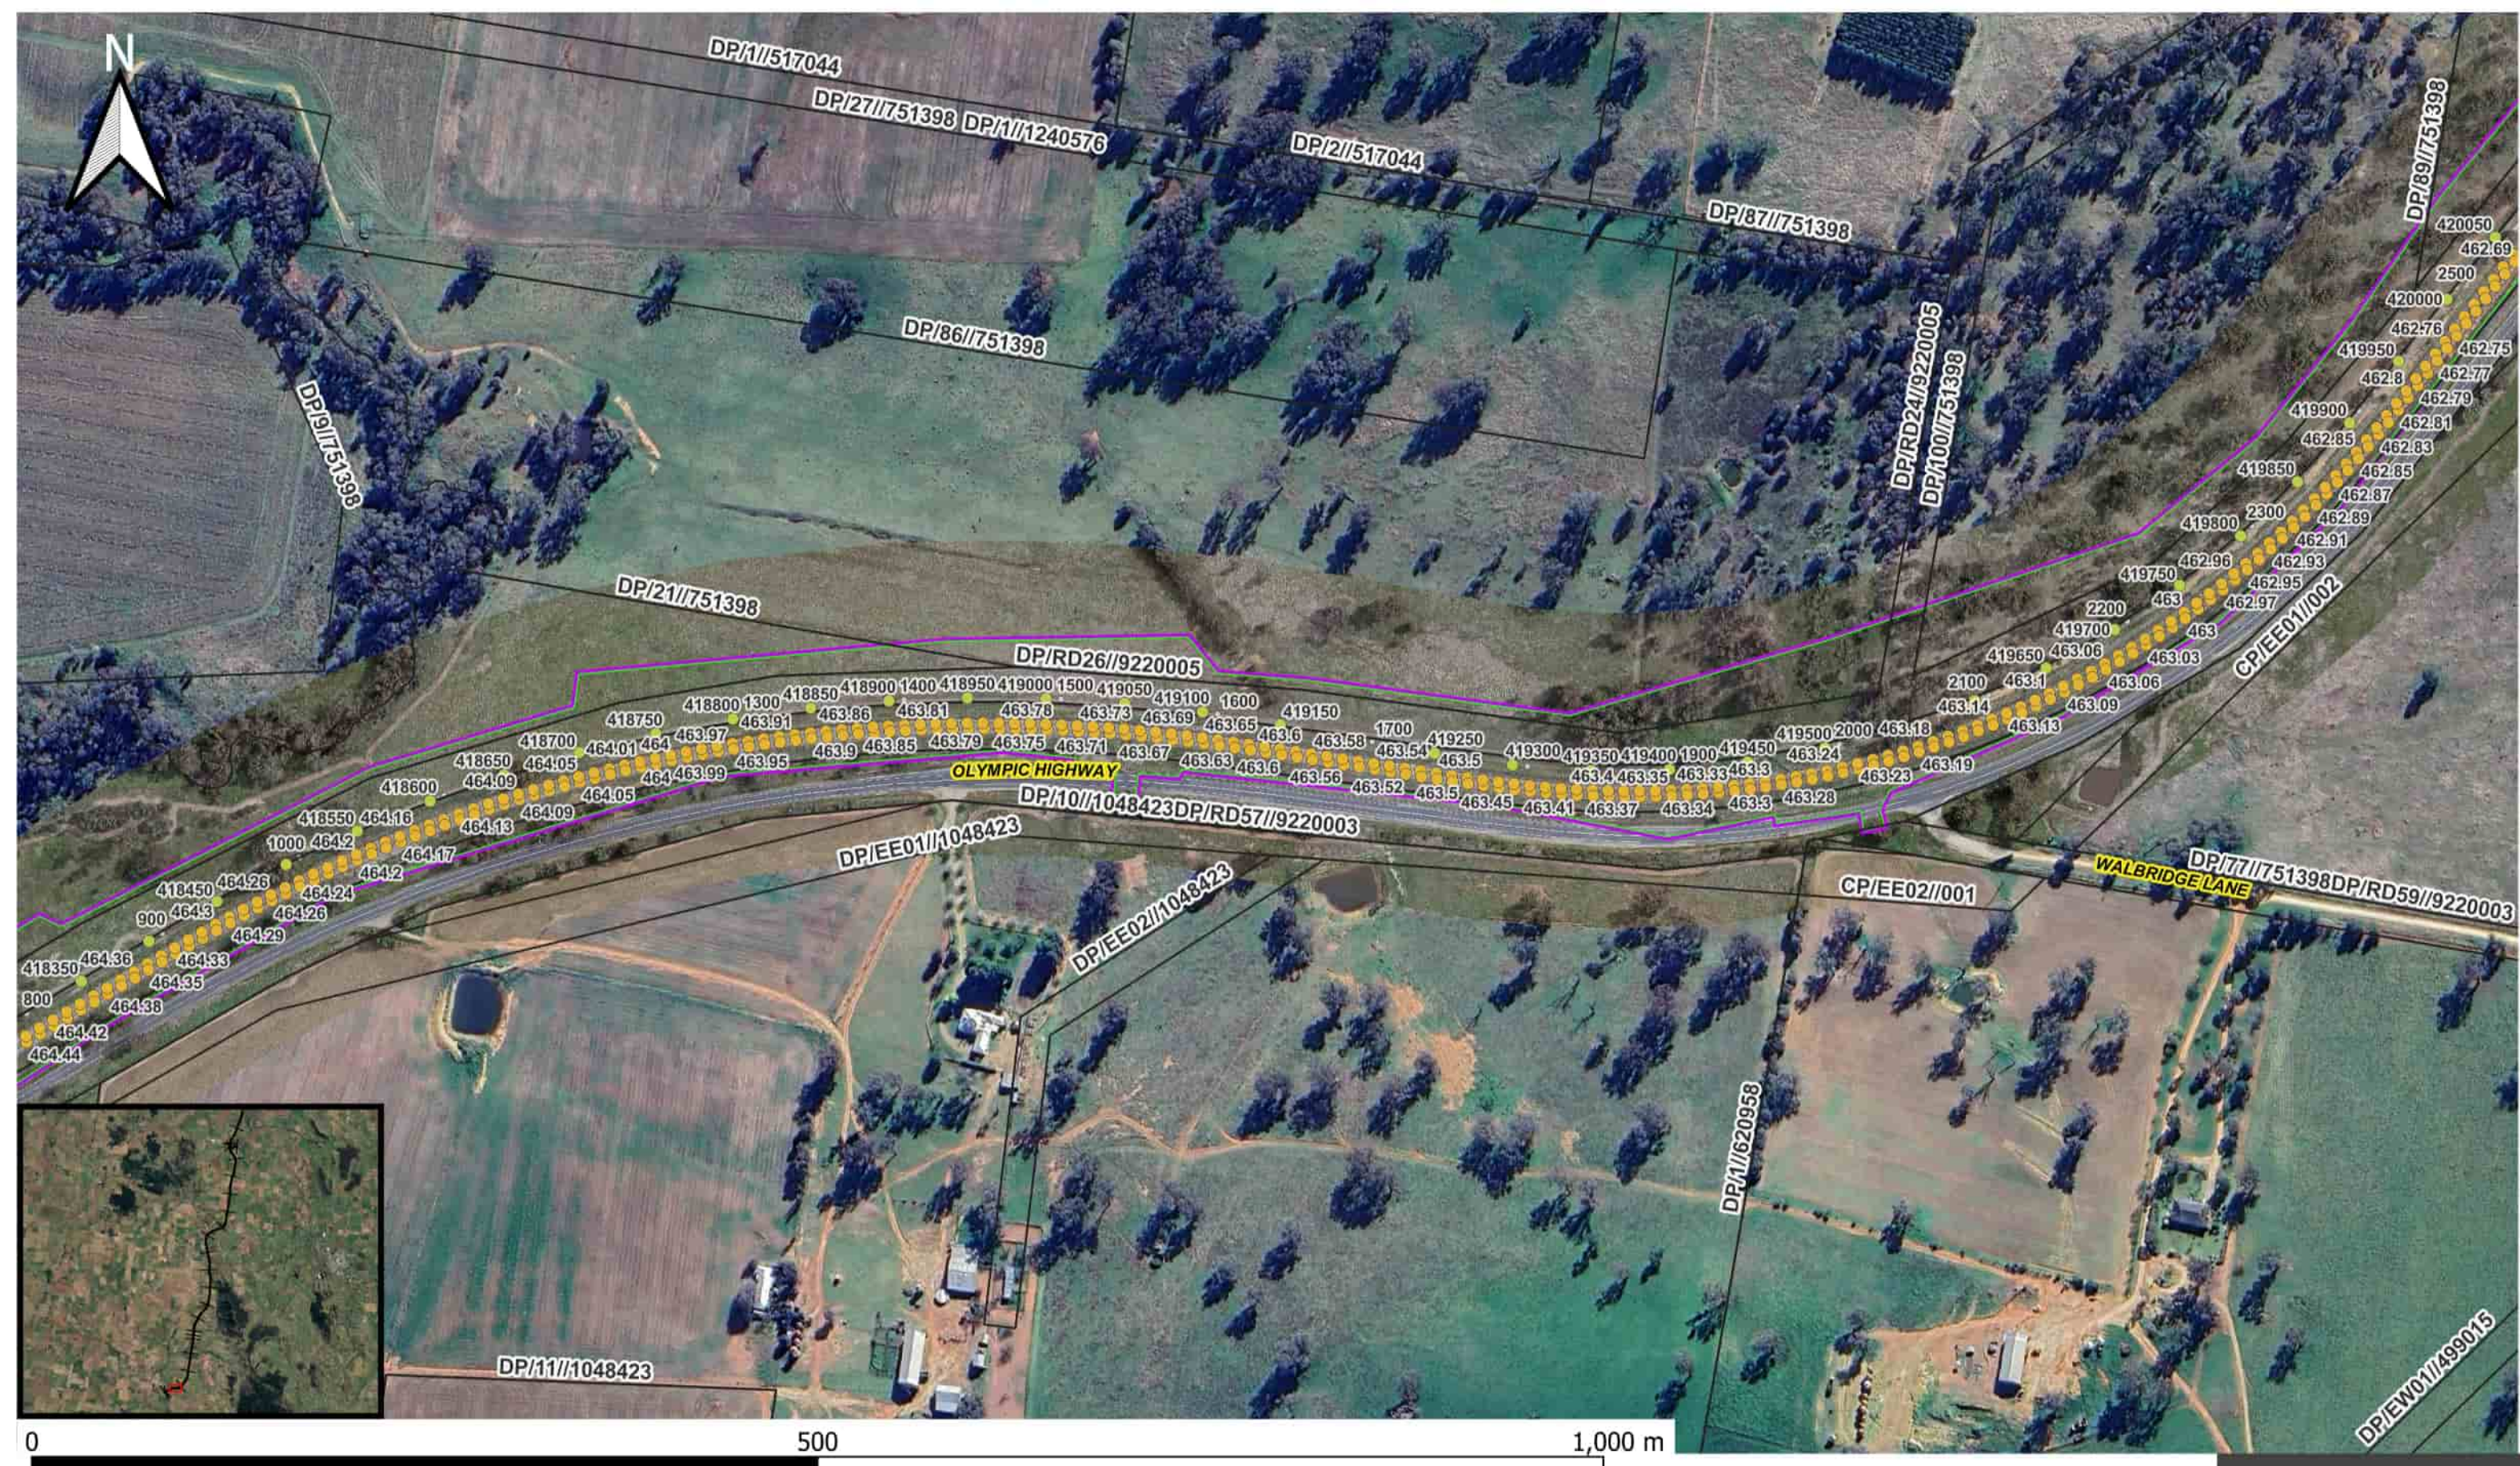

Legend

- Road Names   Other Boundaries   Chainages   ARTC Kilometrage
- Cadastre   • Chainage (Project, m)
- Premise Boundary



PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend

- Road Names

Other Boundaries

Chainages
- Cadastral

Chainage (Project, m)
- Premise Boundary
- ARTC Kilometerage

JOHN

HOLLAND

INLAND

RAIL

PREMISE BOUNDARY MAPS

Date: 19/01/2026

Author: Tess Anastakis

Approver: Trent Doyle

Data Sources: IRPL, JH

Paper: A3

Rev: A



Legend

- Road Names

Other Boundaries

Chainages
- Cadastre

Chainage (Project, m)

Premise Boundary
- ARTC Kilometrage



PREMISE BOUNDARY MAPS

Date: 19/01/2026

Author: Tess Anastakis

Approver: Trent Doyle

Data Sources: IRPL, JH

Paper: A3

Rev: A



- Legend
- |            |                  |                  |
|------------|------------------|------------------|
| Road Names | Other Boundaries | Chainages        |
|            | Cadastral        | ARTC Kilometrage |
|            | Premise Boundary |                  |

PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



Legend

|            |                  |                  |
|------------|------------------|------------------|
| Road Names | Other Boundaries | Chainages        |
|            | Cadastral        | ARTC Kilometrage |
|            | Premise Boundary |                  |



**PREMISE BOUNDARY MAPS**

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH



Legend

- Road Names

Other Boundaries

Chainages
- Cadastre

Premise Boundary
- ARTC Kilometrage



PREMISE BOUNDARY MAPS

Date: 19/01/2026

Author: Tess Anastakis

Approver: Trent Doyle

Data Sources: IRPL, JH

Paper: A3

Rev: A



Legend

|            |                  |                  |
|------------|------------------|------------------|
| Road Names | Other Boundaries | Chainages        |
|            | Cadastral        | ARTC Kilometrage |
|            | Premise Boundary |                  |

PREMISE BOUNDARY MAPS

Date: 19/01/2026  
Author: Tess Anastakis  
Approver: Trent Doyle  
Data Sources: IRPL, JH

Paper: A3  
Rev: A



# Appendix B EPL Water Discharge Points


**Legend**


Site Environmental Plans (SEPs)

- Discharge Points - EPL
- Road Names

CIZ


- CIZ (Rev 4)

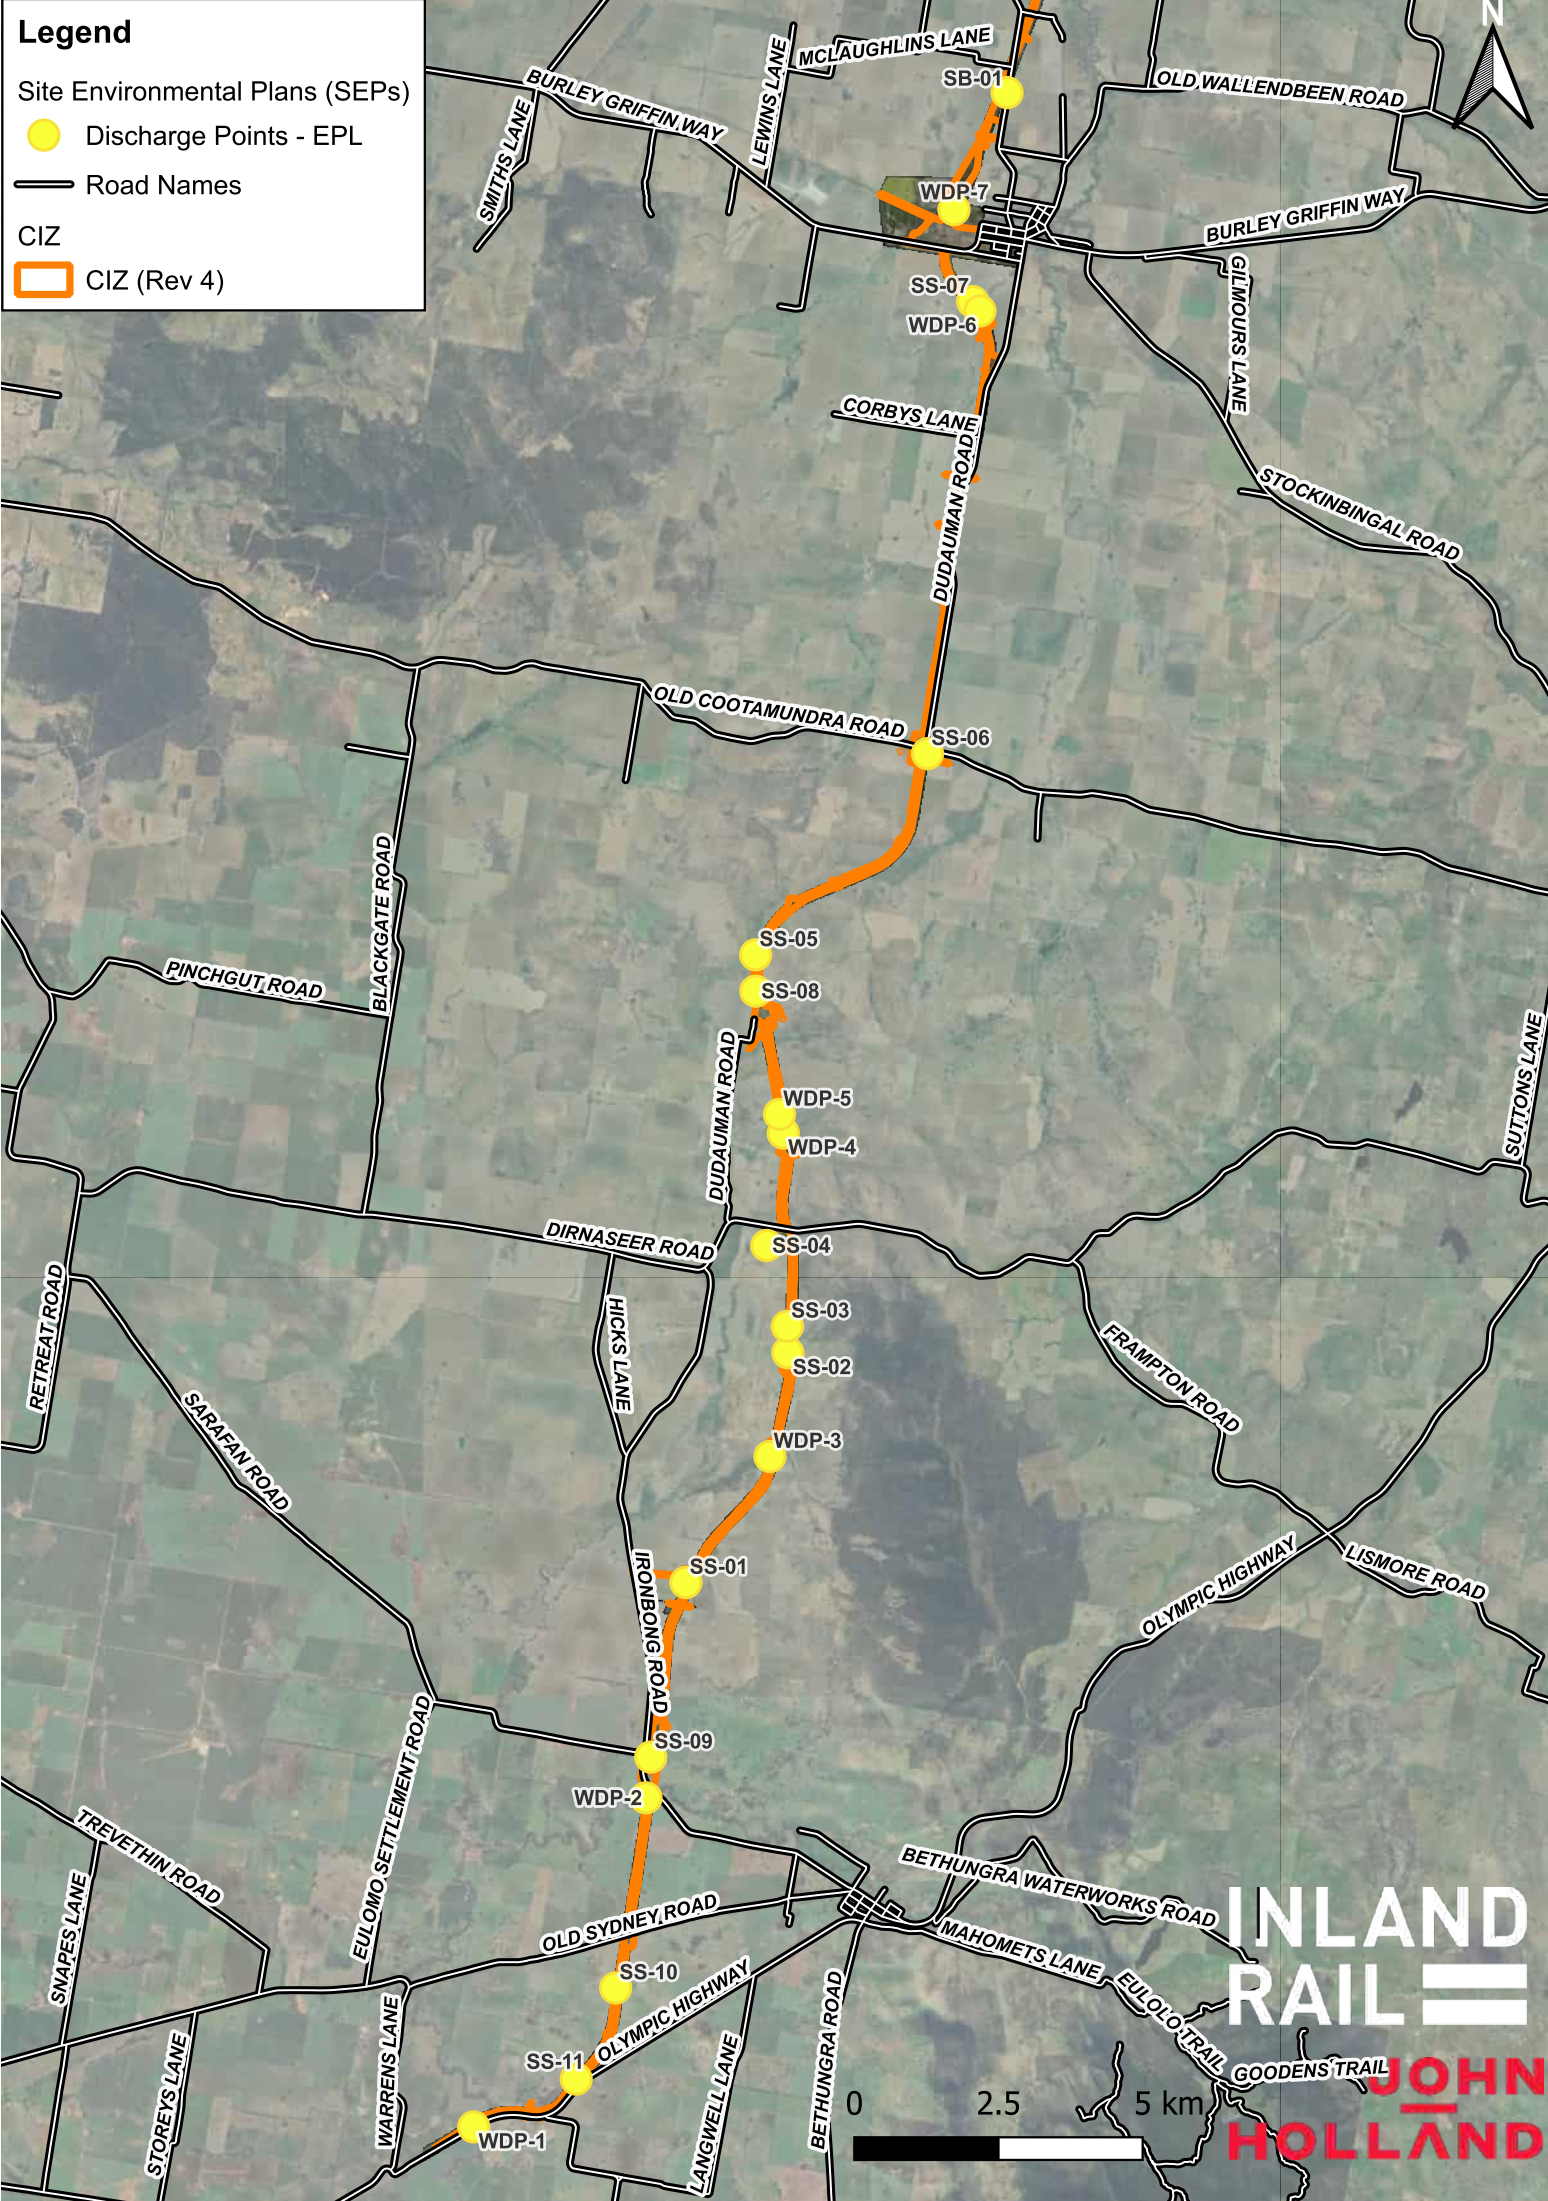

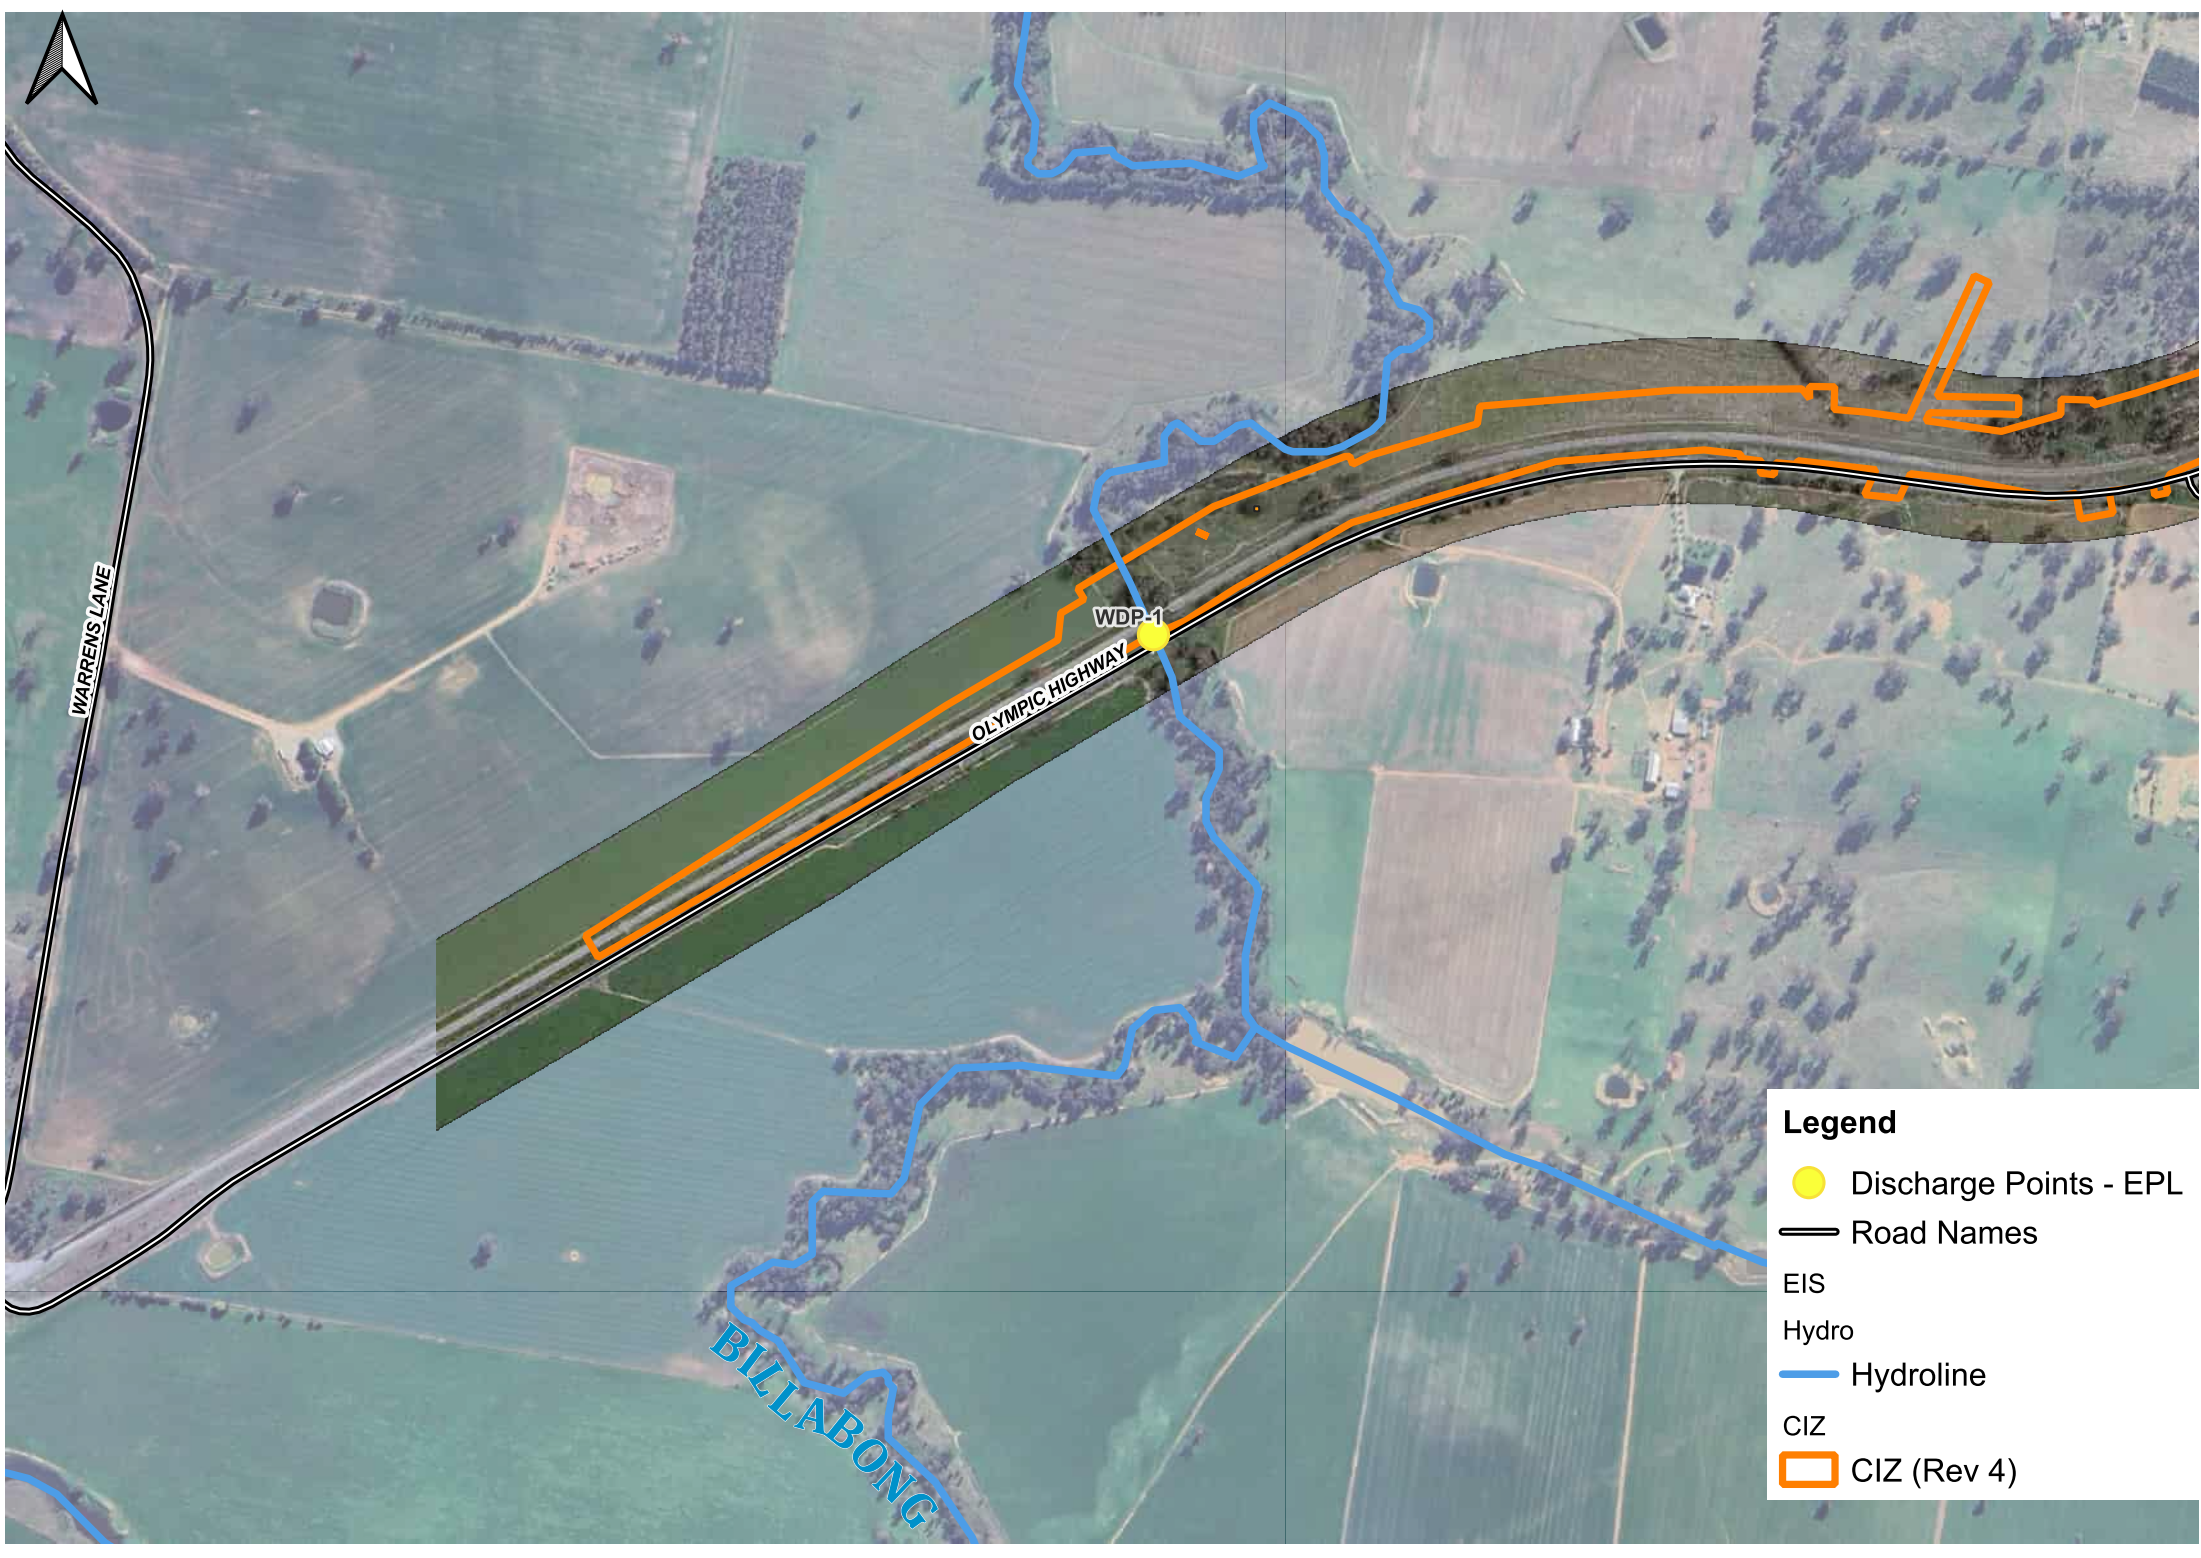

**Legend**

-  Discharge Points - EPL
-  Road Names
- EIS
- Hydro
-  Hydroline
- CIZ
-  CIZ (Rev 4)

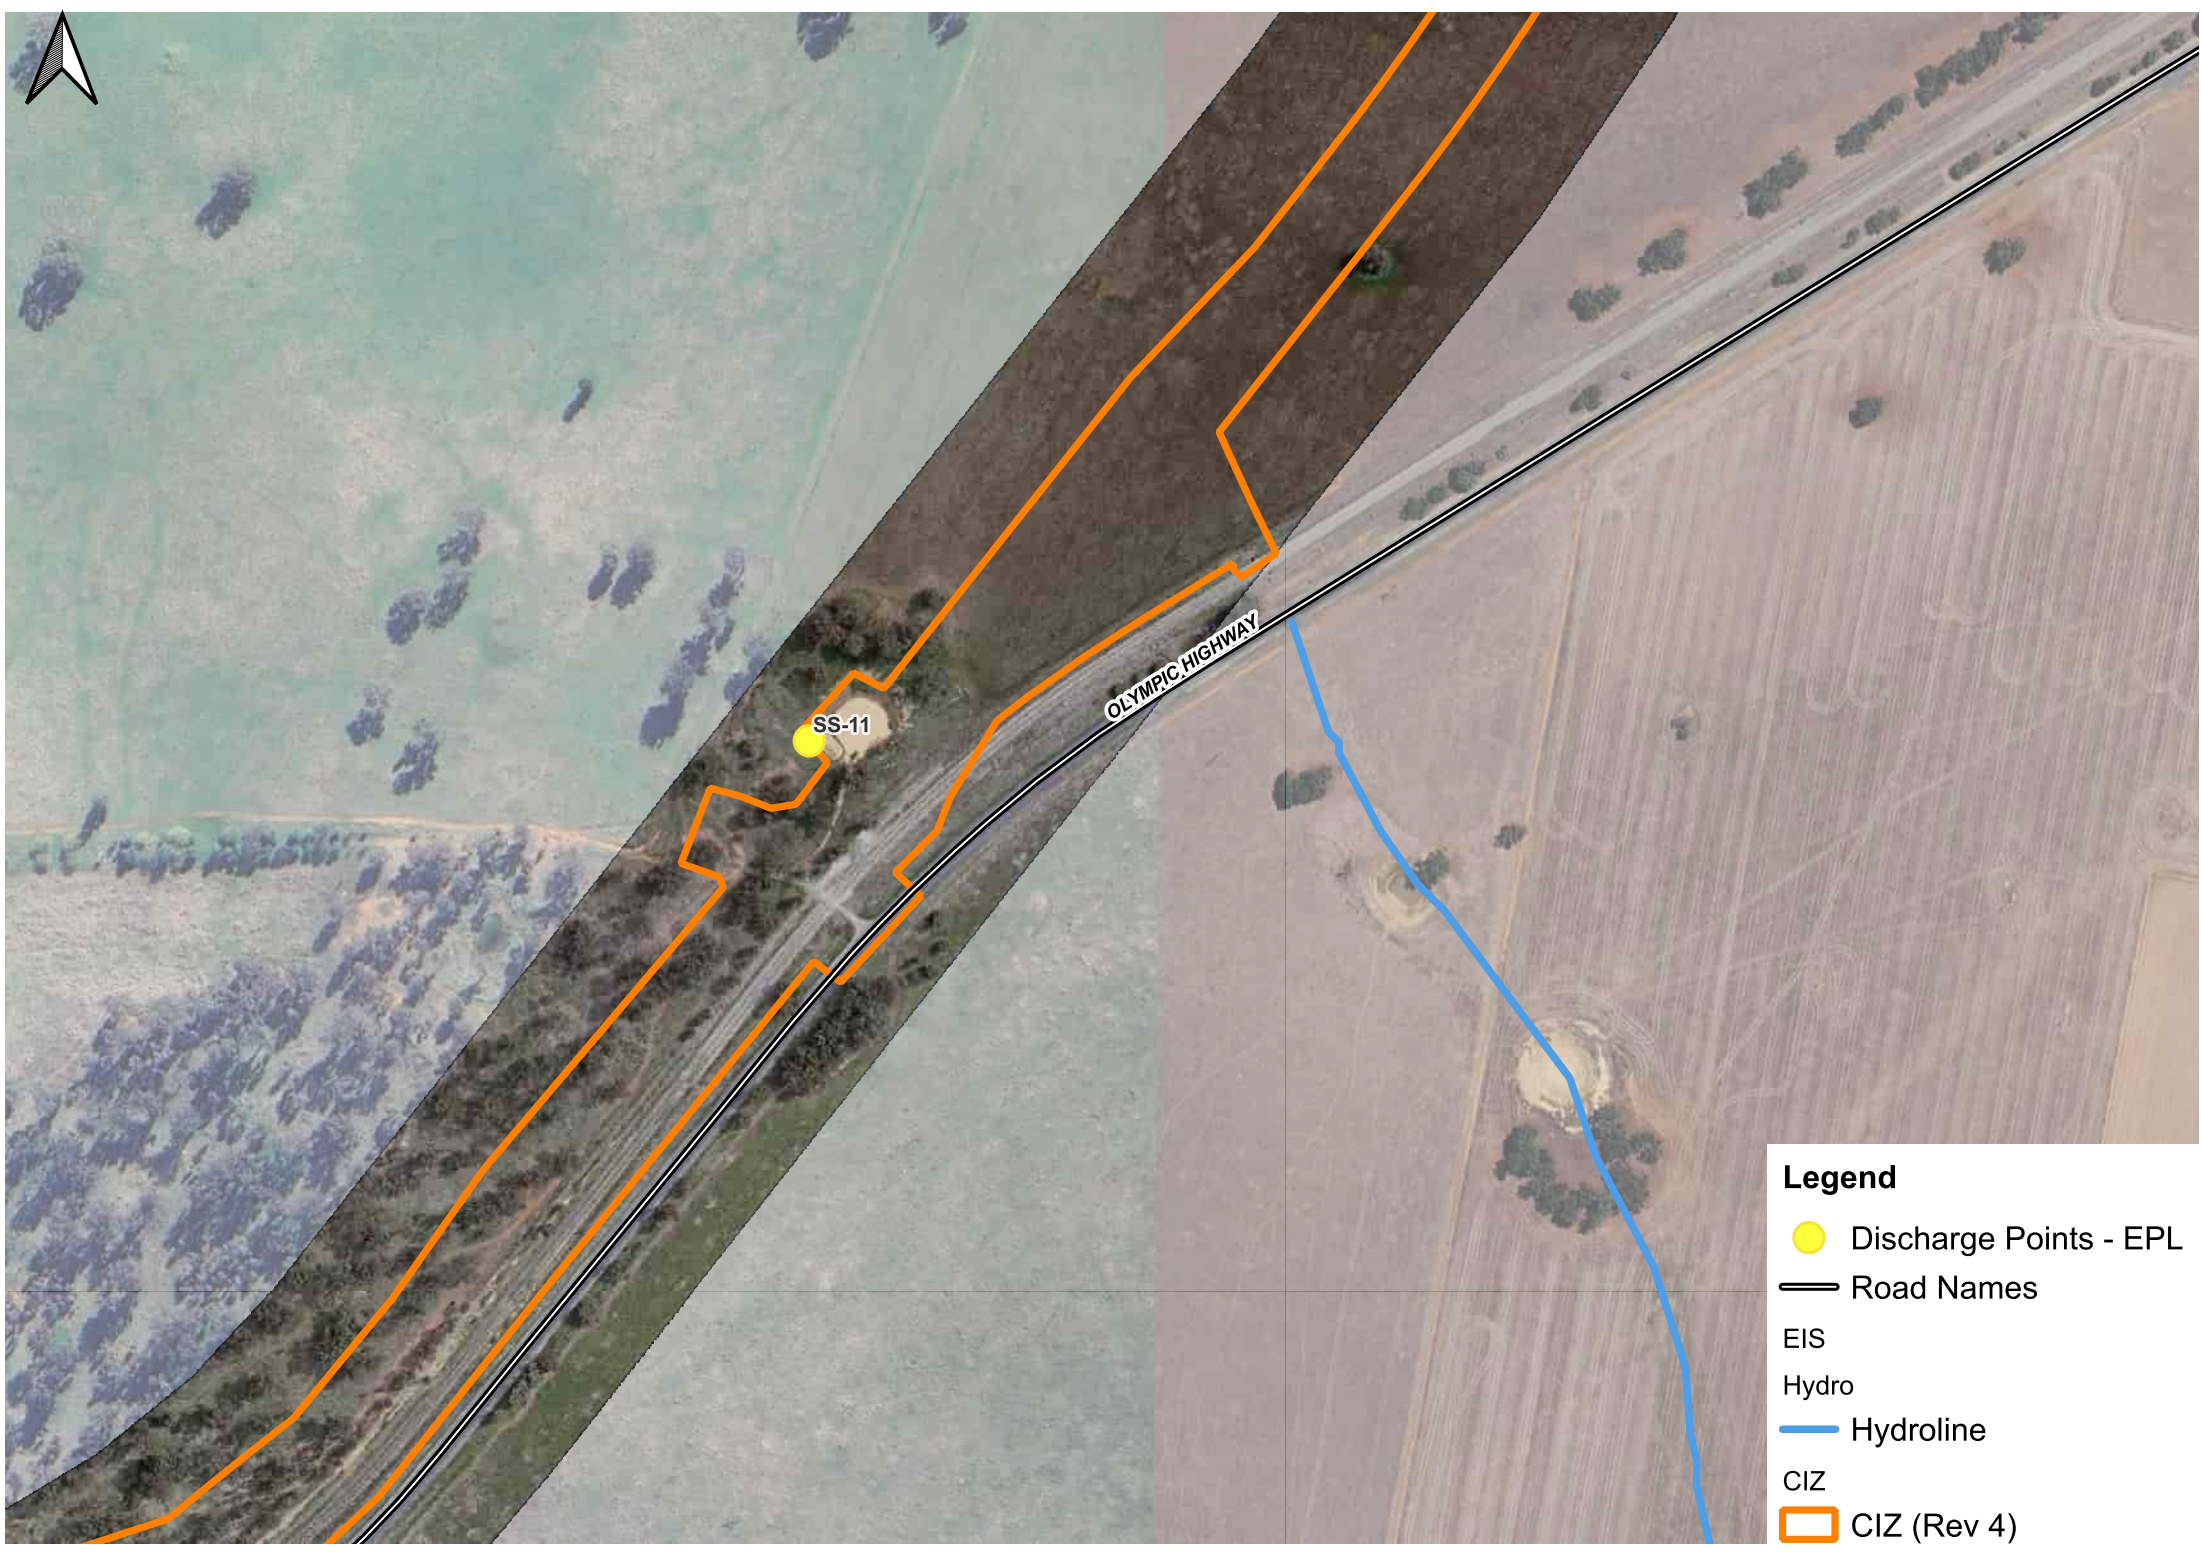

**Legend**

-  Discharge Points - EPL
-  Road Names
- EIS
- Hydro
-  Hydroline
- CIZ
-  CIZ (Rev 4)



**Legend**

- Discharge Points - EPL
- Rail Features
  - I2S KM Chainage
- EIS
  - Hydro
    - Hydroline
- CIZ
  - CIZ (Rev 4)




**Legend**

-  Discharge Points - EPL
-  Road Names
- Rail Features
  -  I2S KM Chainage
- EIS
- Hydro
  -  Hydroline
- CIZ
  -  CIZ (Rev 4)




**Legend**

-  Discharge Points - EPL
-  Road Names
- Rail Features
  -  I2S KM Chainage
- EIS
- Hydro
  -  Hydroline
- CIZ
  -  CIZ (Rev 4)

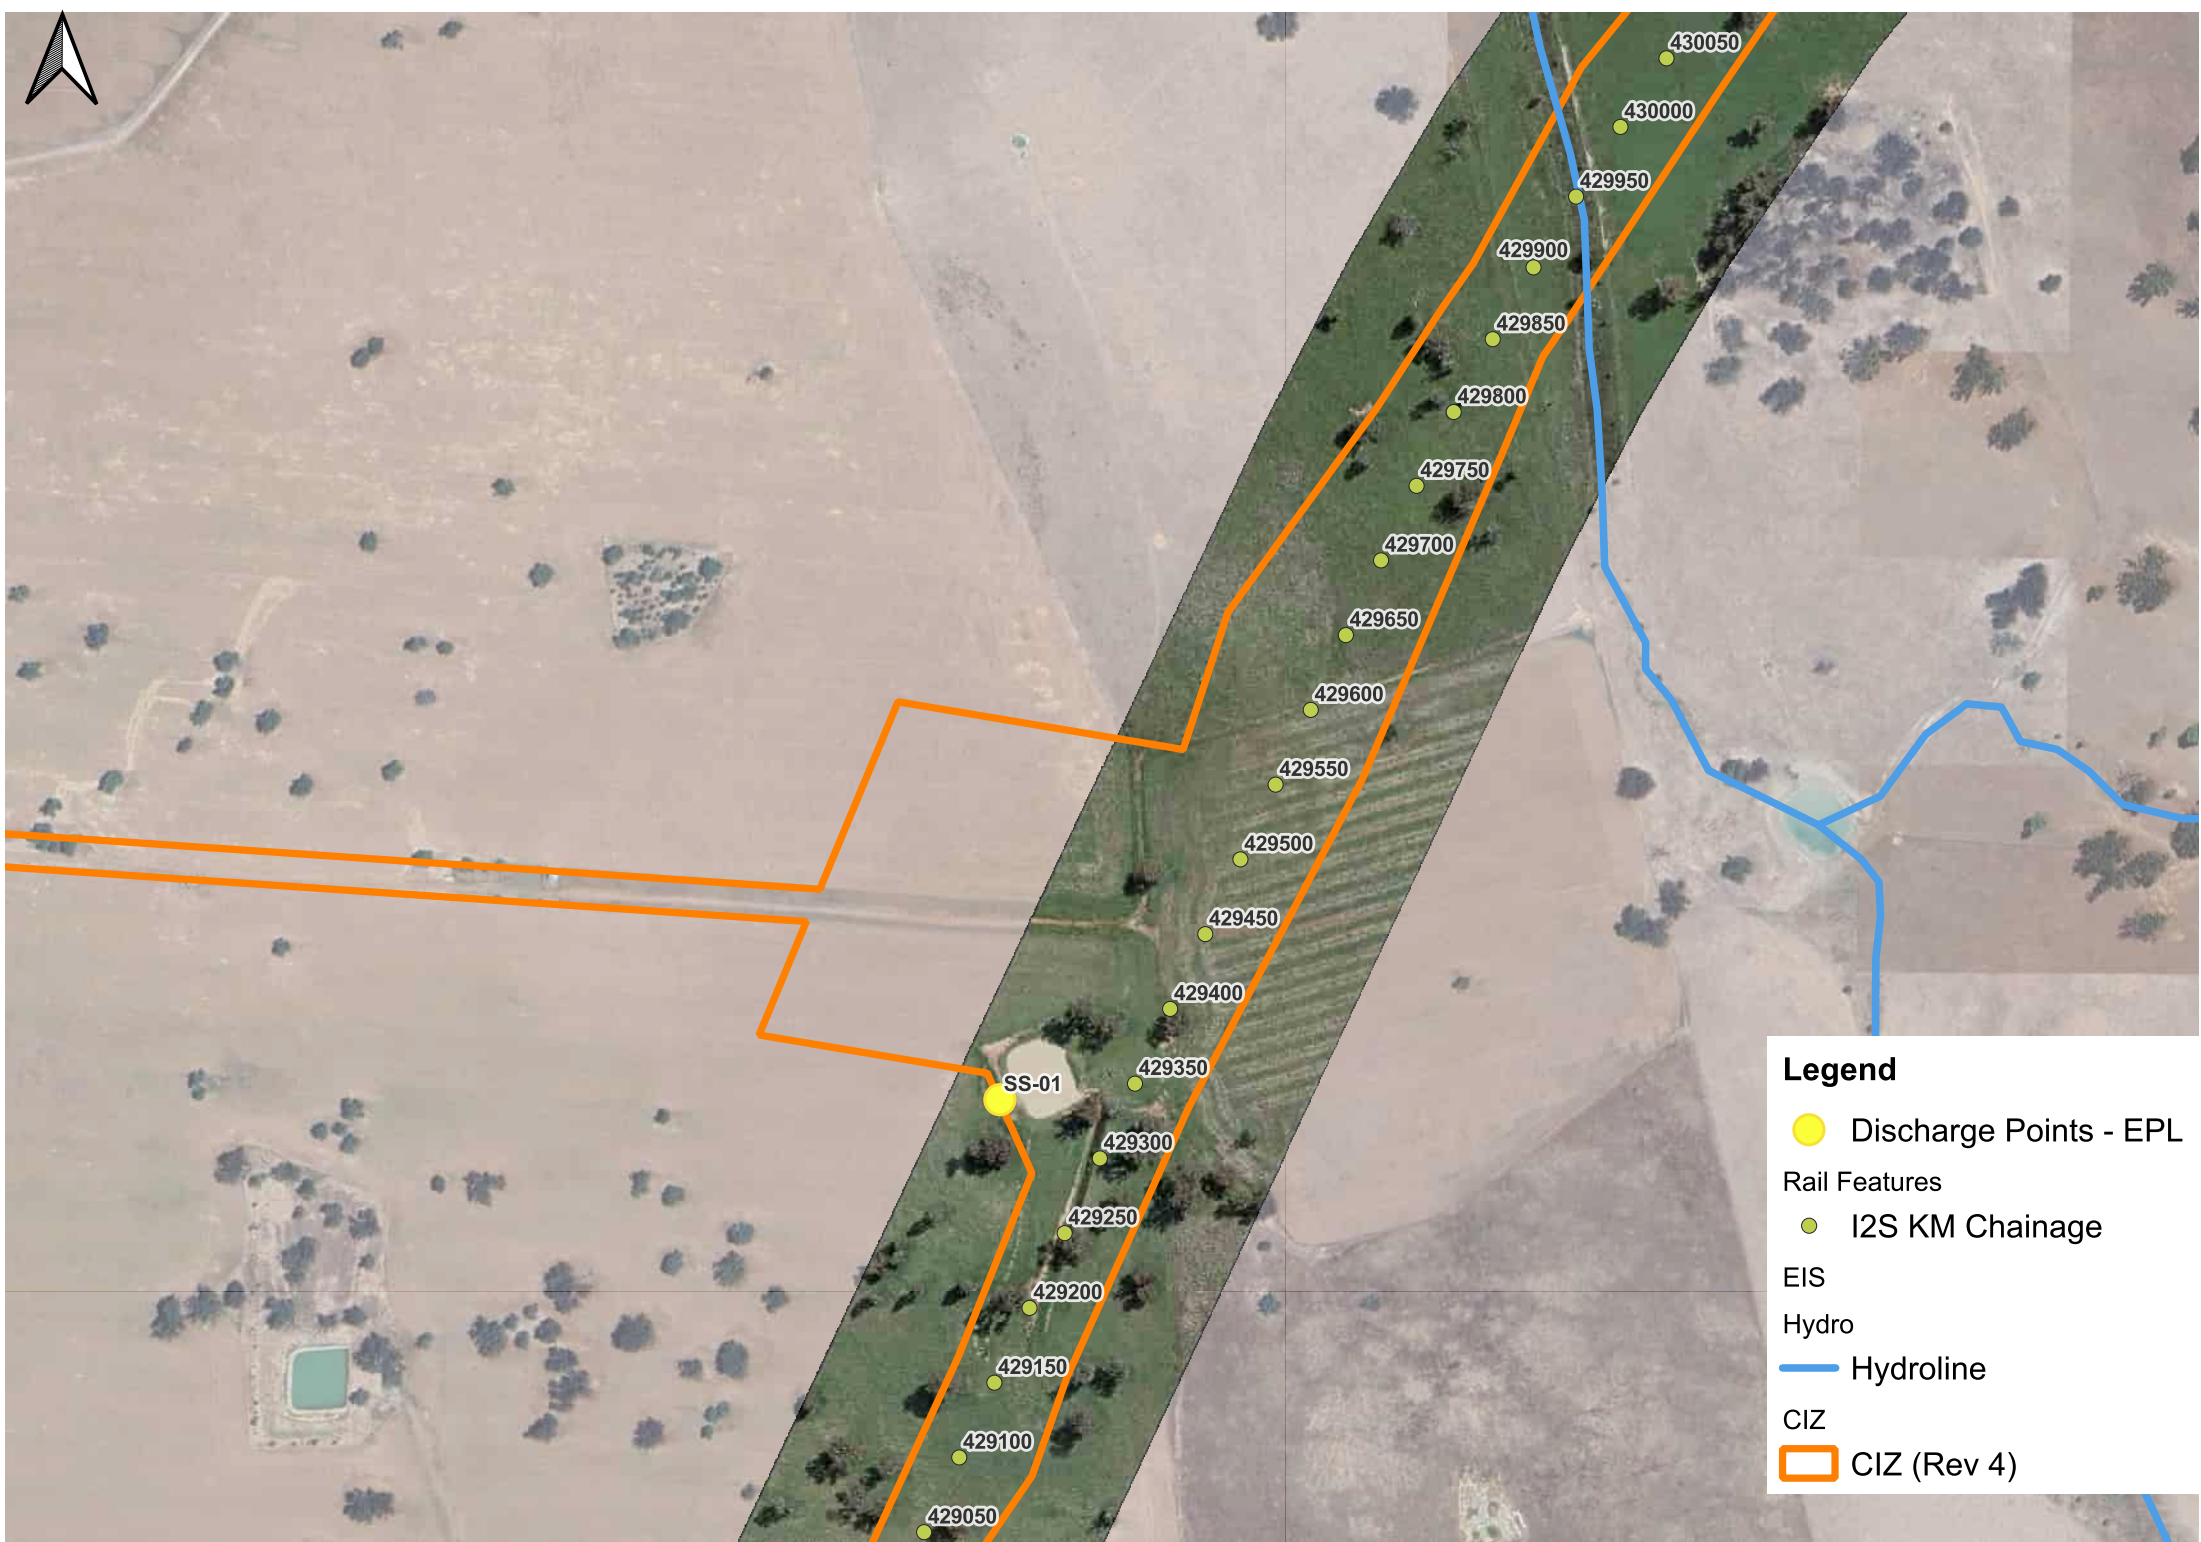

**Legend**

- Discharge Points - EPL
- Rail Features
  - I2S KM Chainage
- EIS
  - Hydro
    - Hydroline
- CIZ
  - CIZ (Rev 4)

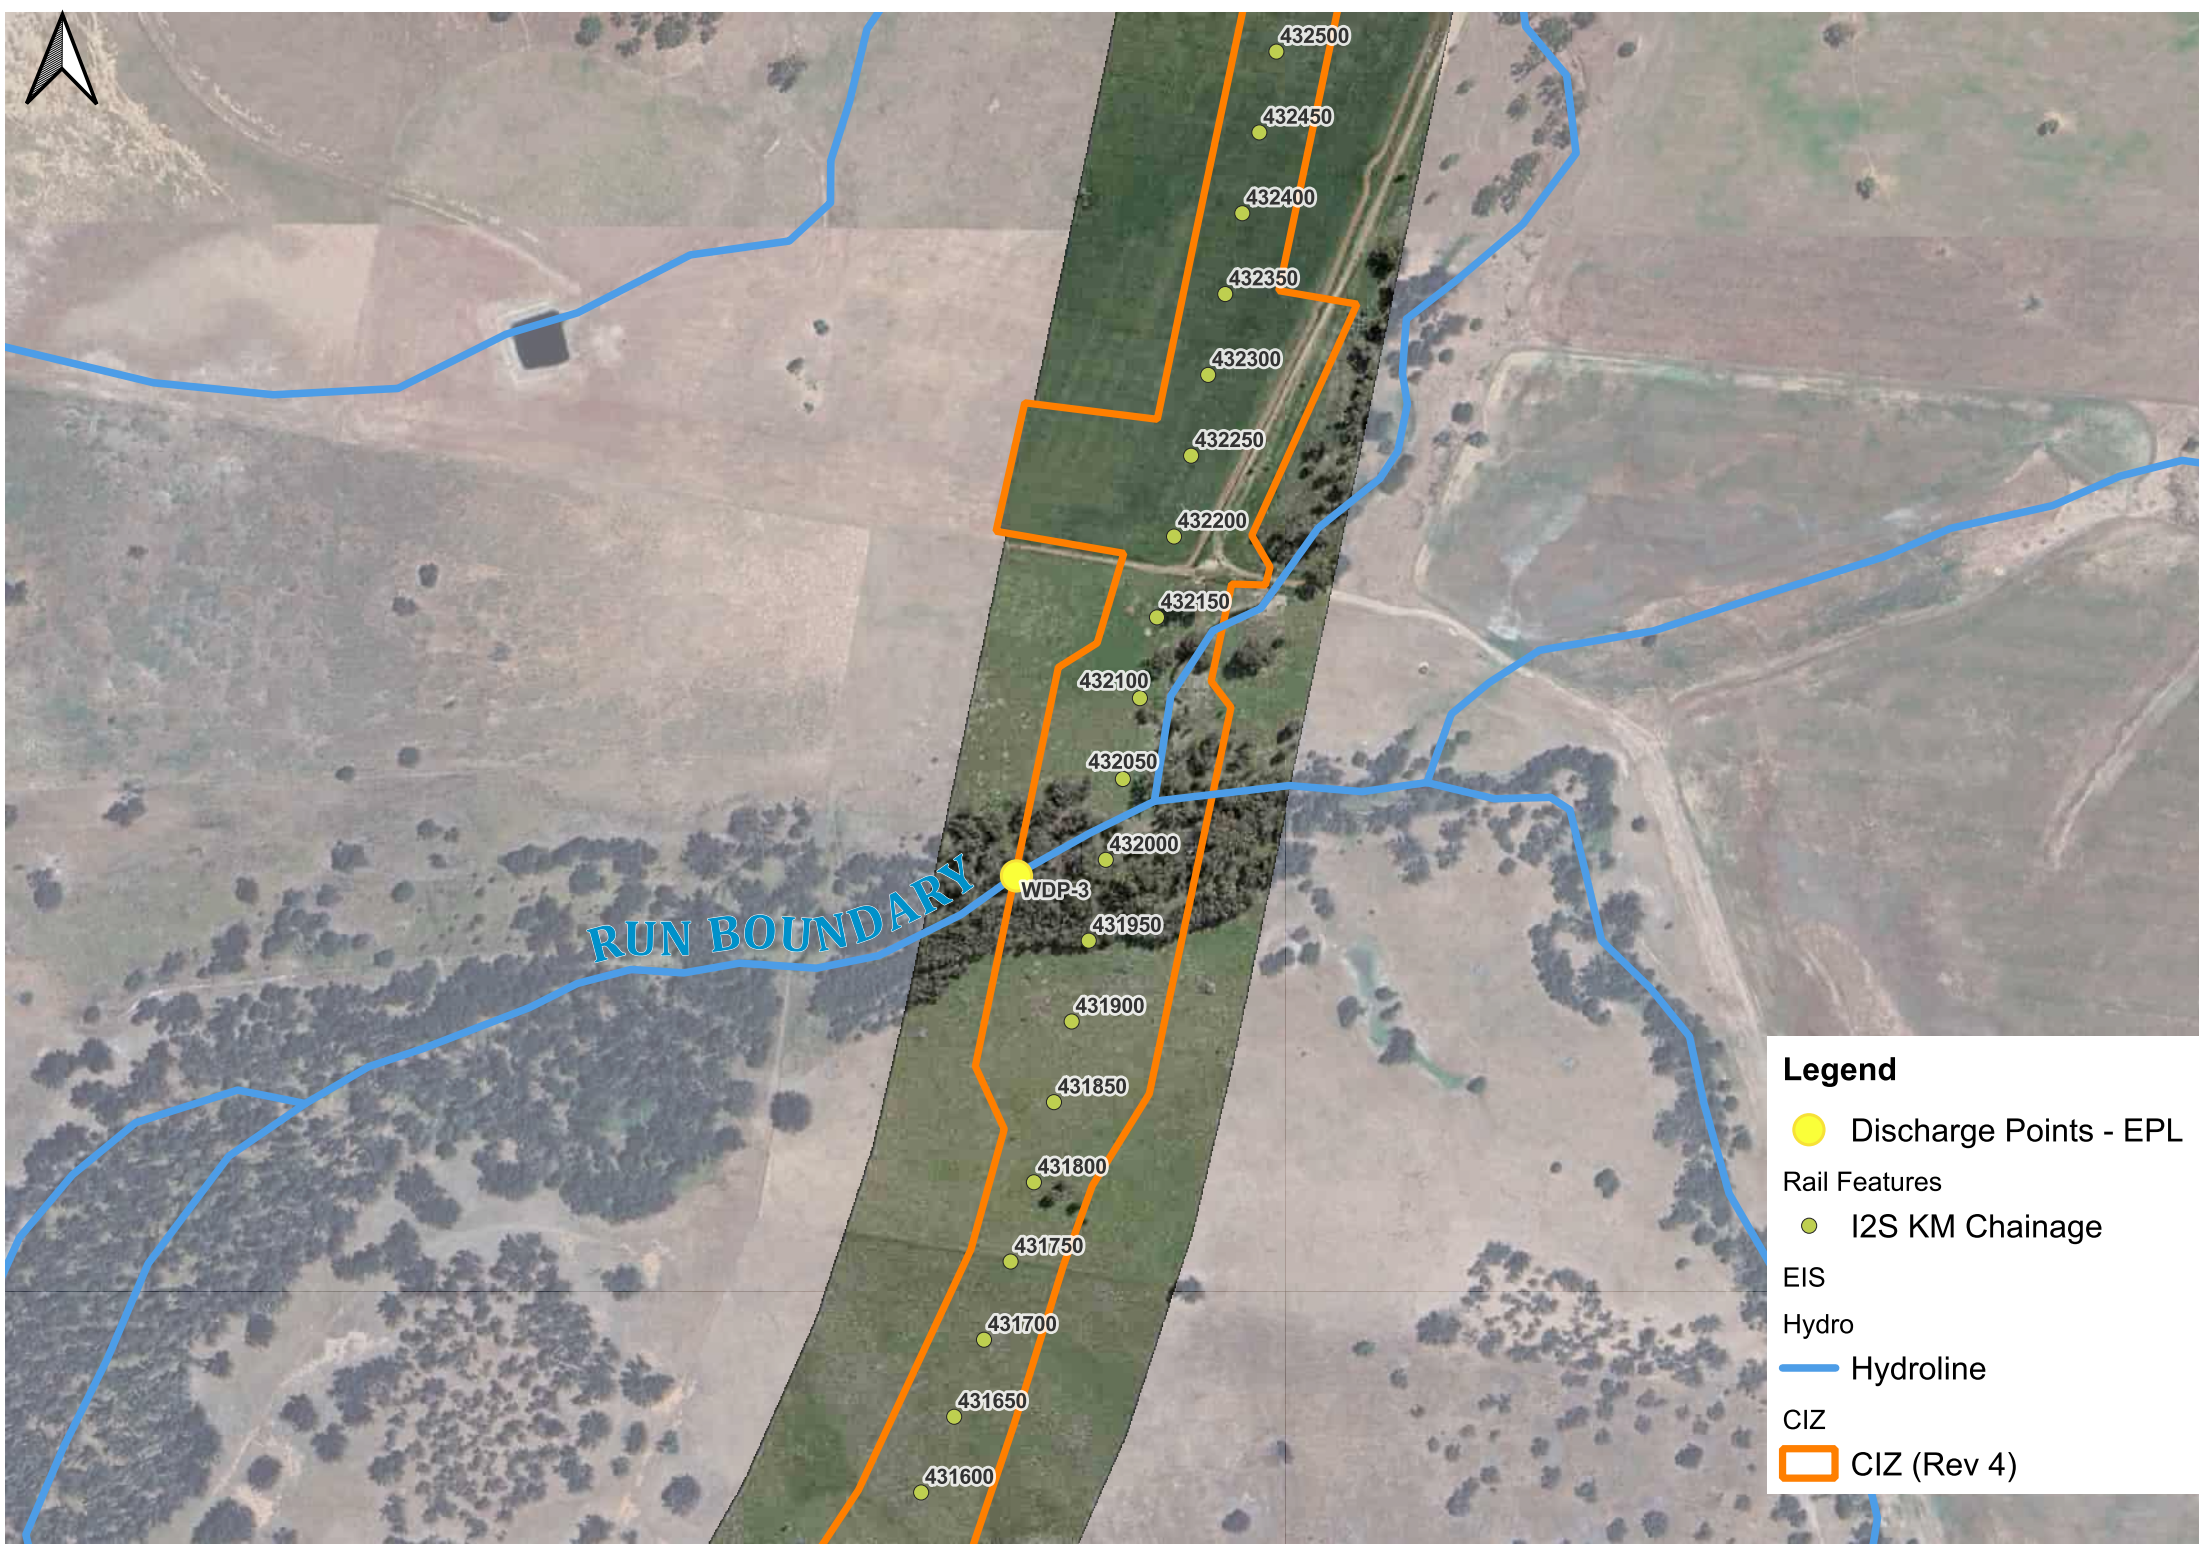


RUN BOUNDARY

WDP-3

- 432500
- 432450
- 432400
- 432350
- 432300
- 432250
- 432200
- 432150
- 432100
- 432050
- 432000
- 431950
- 431900
- 431850
- 431800
- 431750
- 431700
- 431650
- 431600


**Legend**

- Discharge Points - EPL
- Rail Features
  - I2S KM Chainage
- EIS
  - Hydro
- CIZ
  - CIZ (Rev 4)

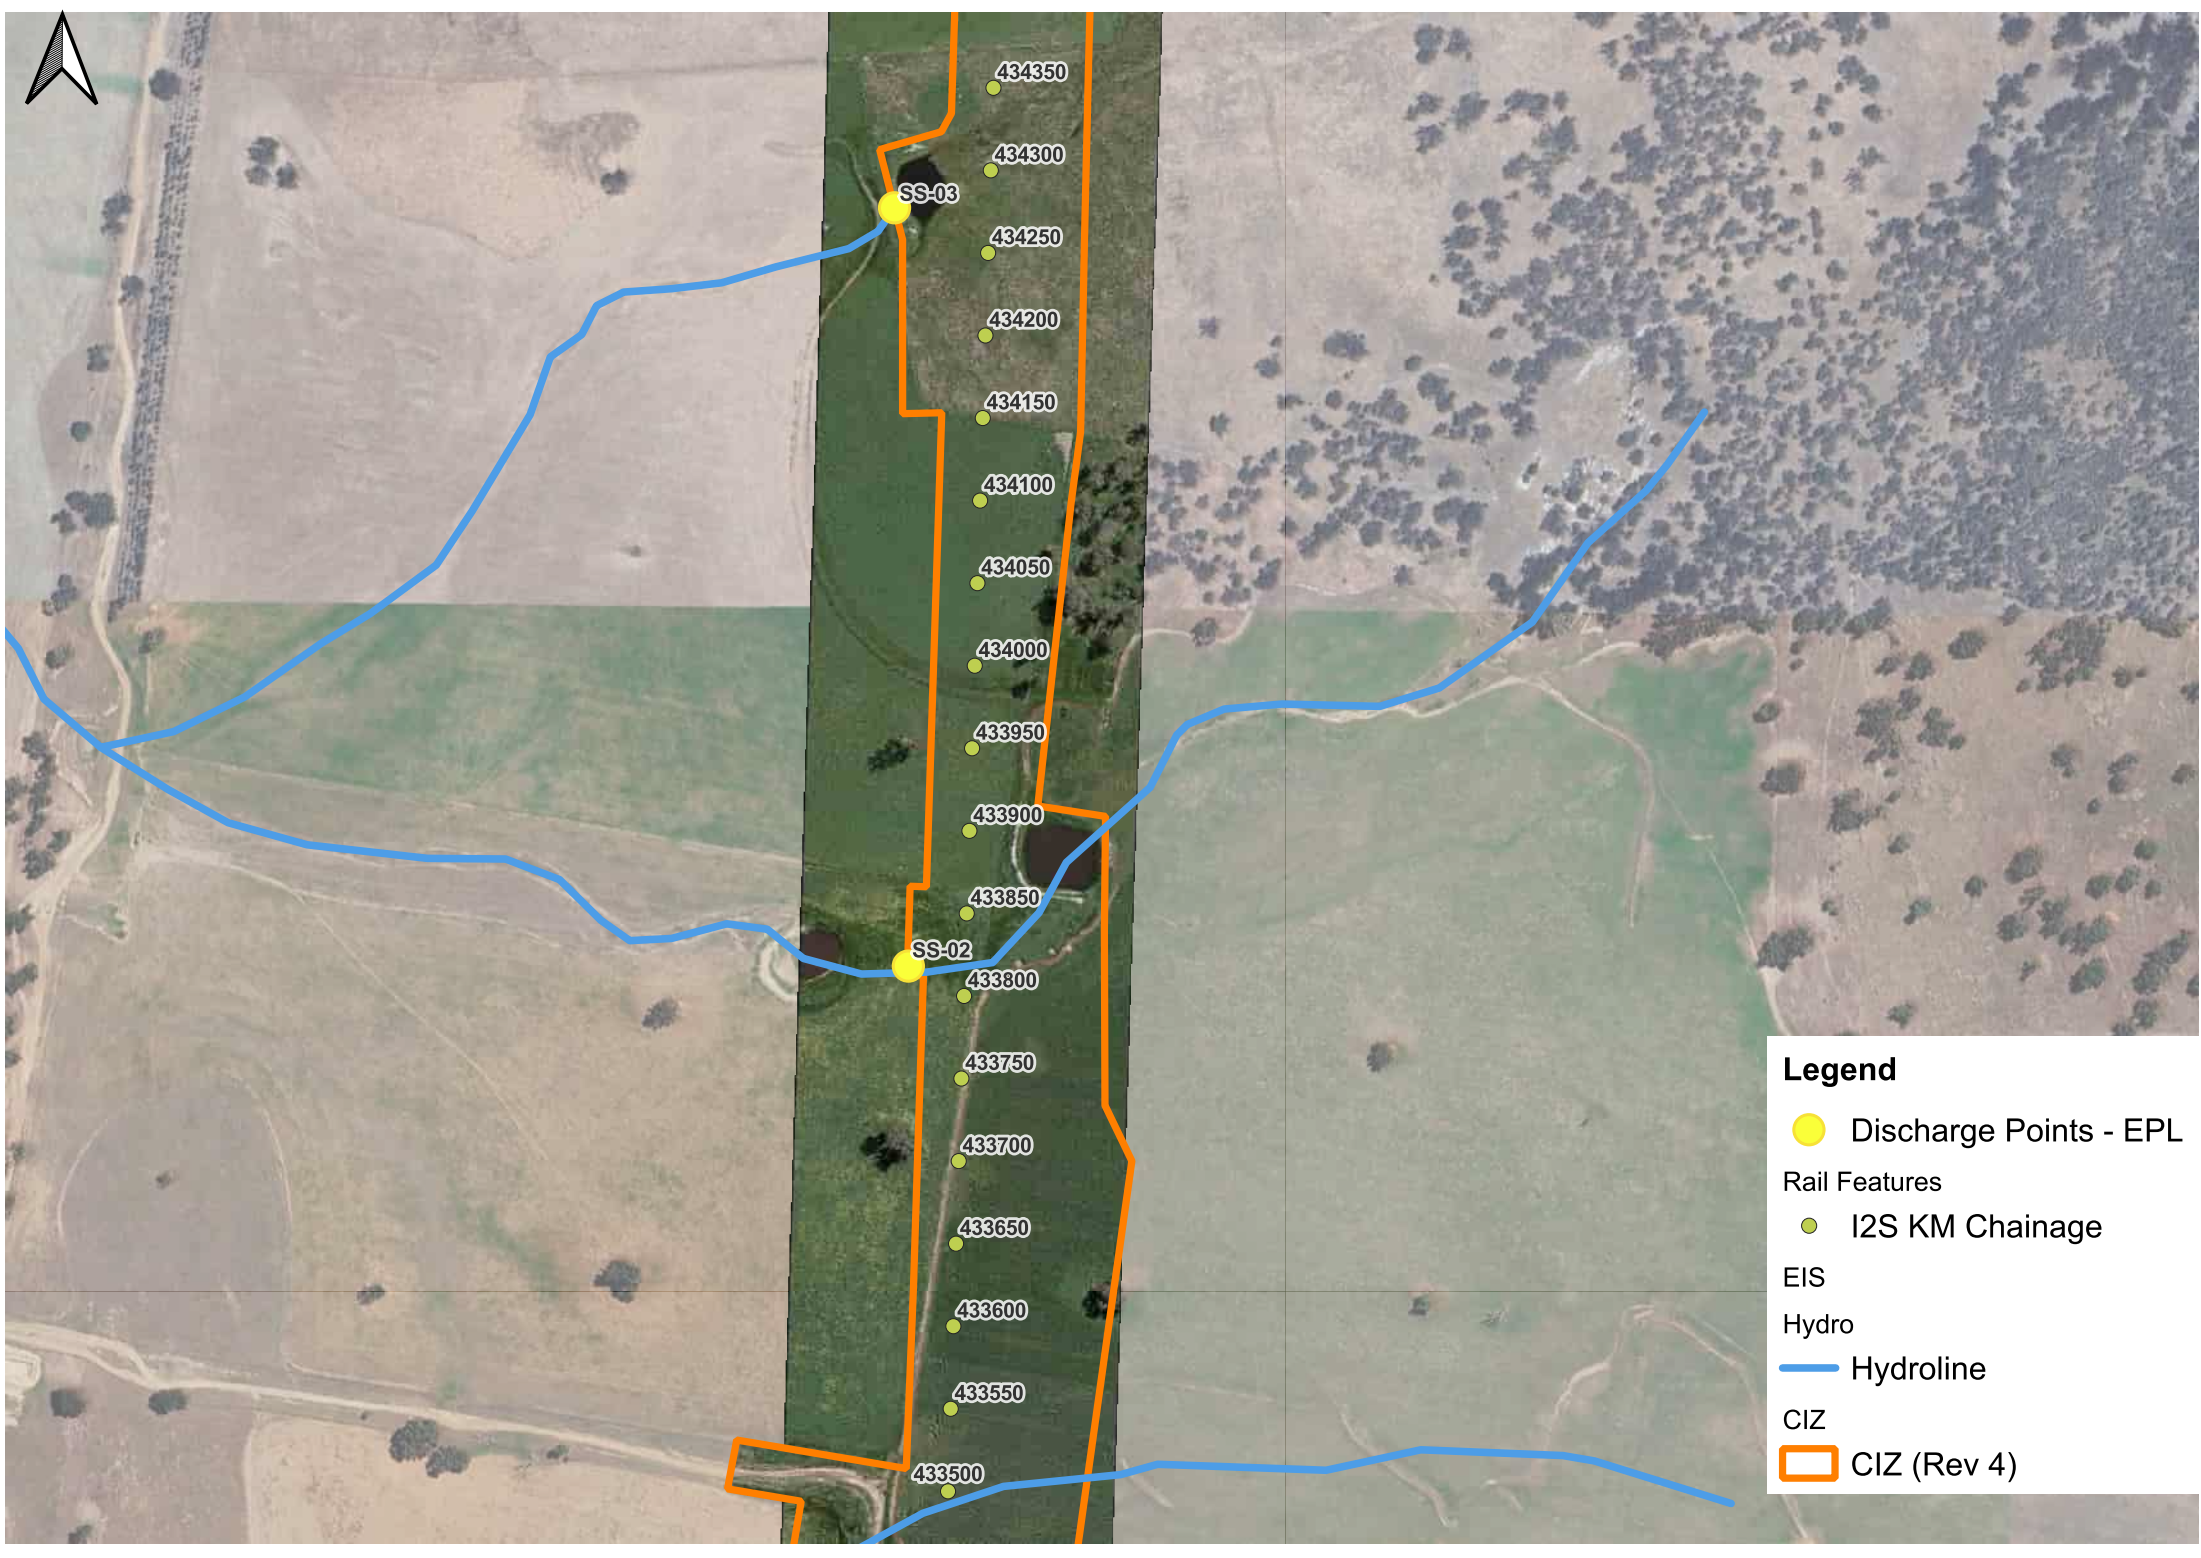

**Legend**

- Discharge Points - EPL
- Rail Features
  - I2S KM Chainage
- EIS
  - Hydro
    - Hydroline
- CIZ
  - CIZ (Rev 4)

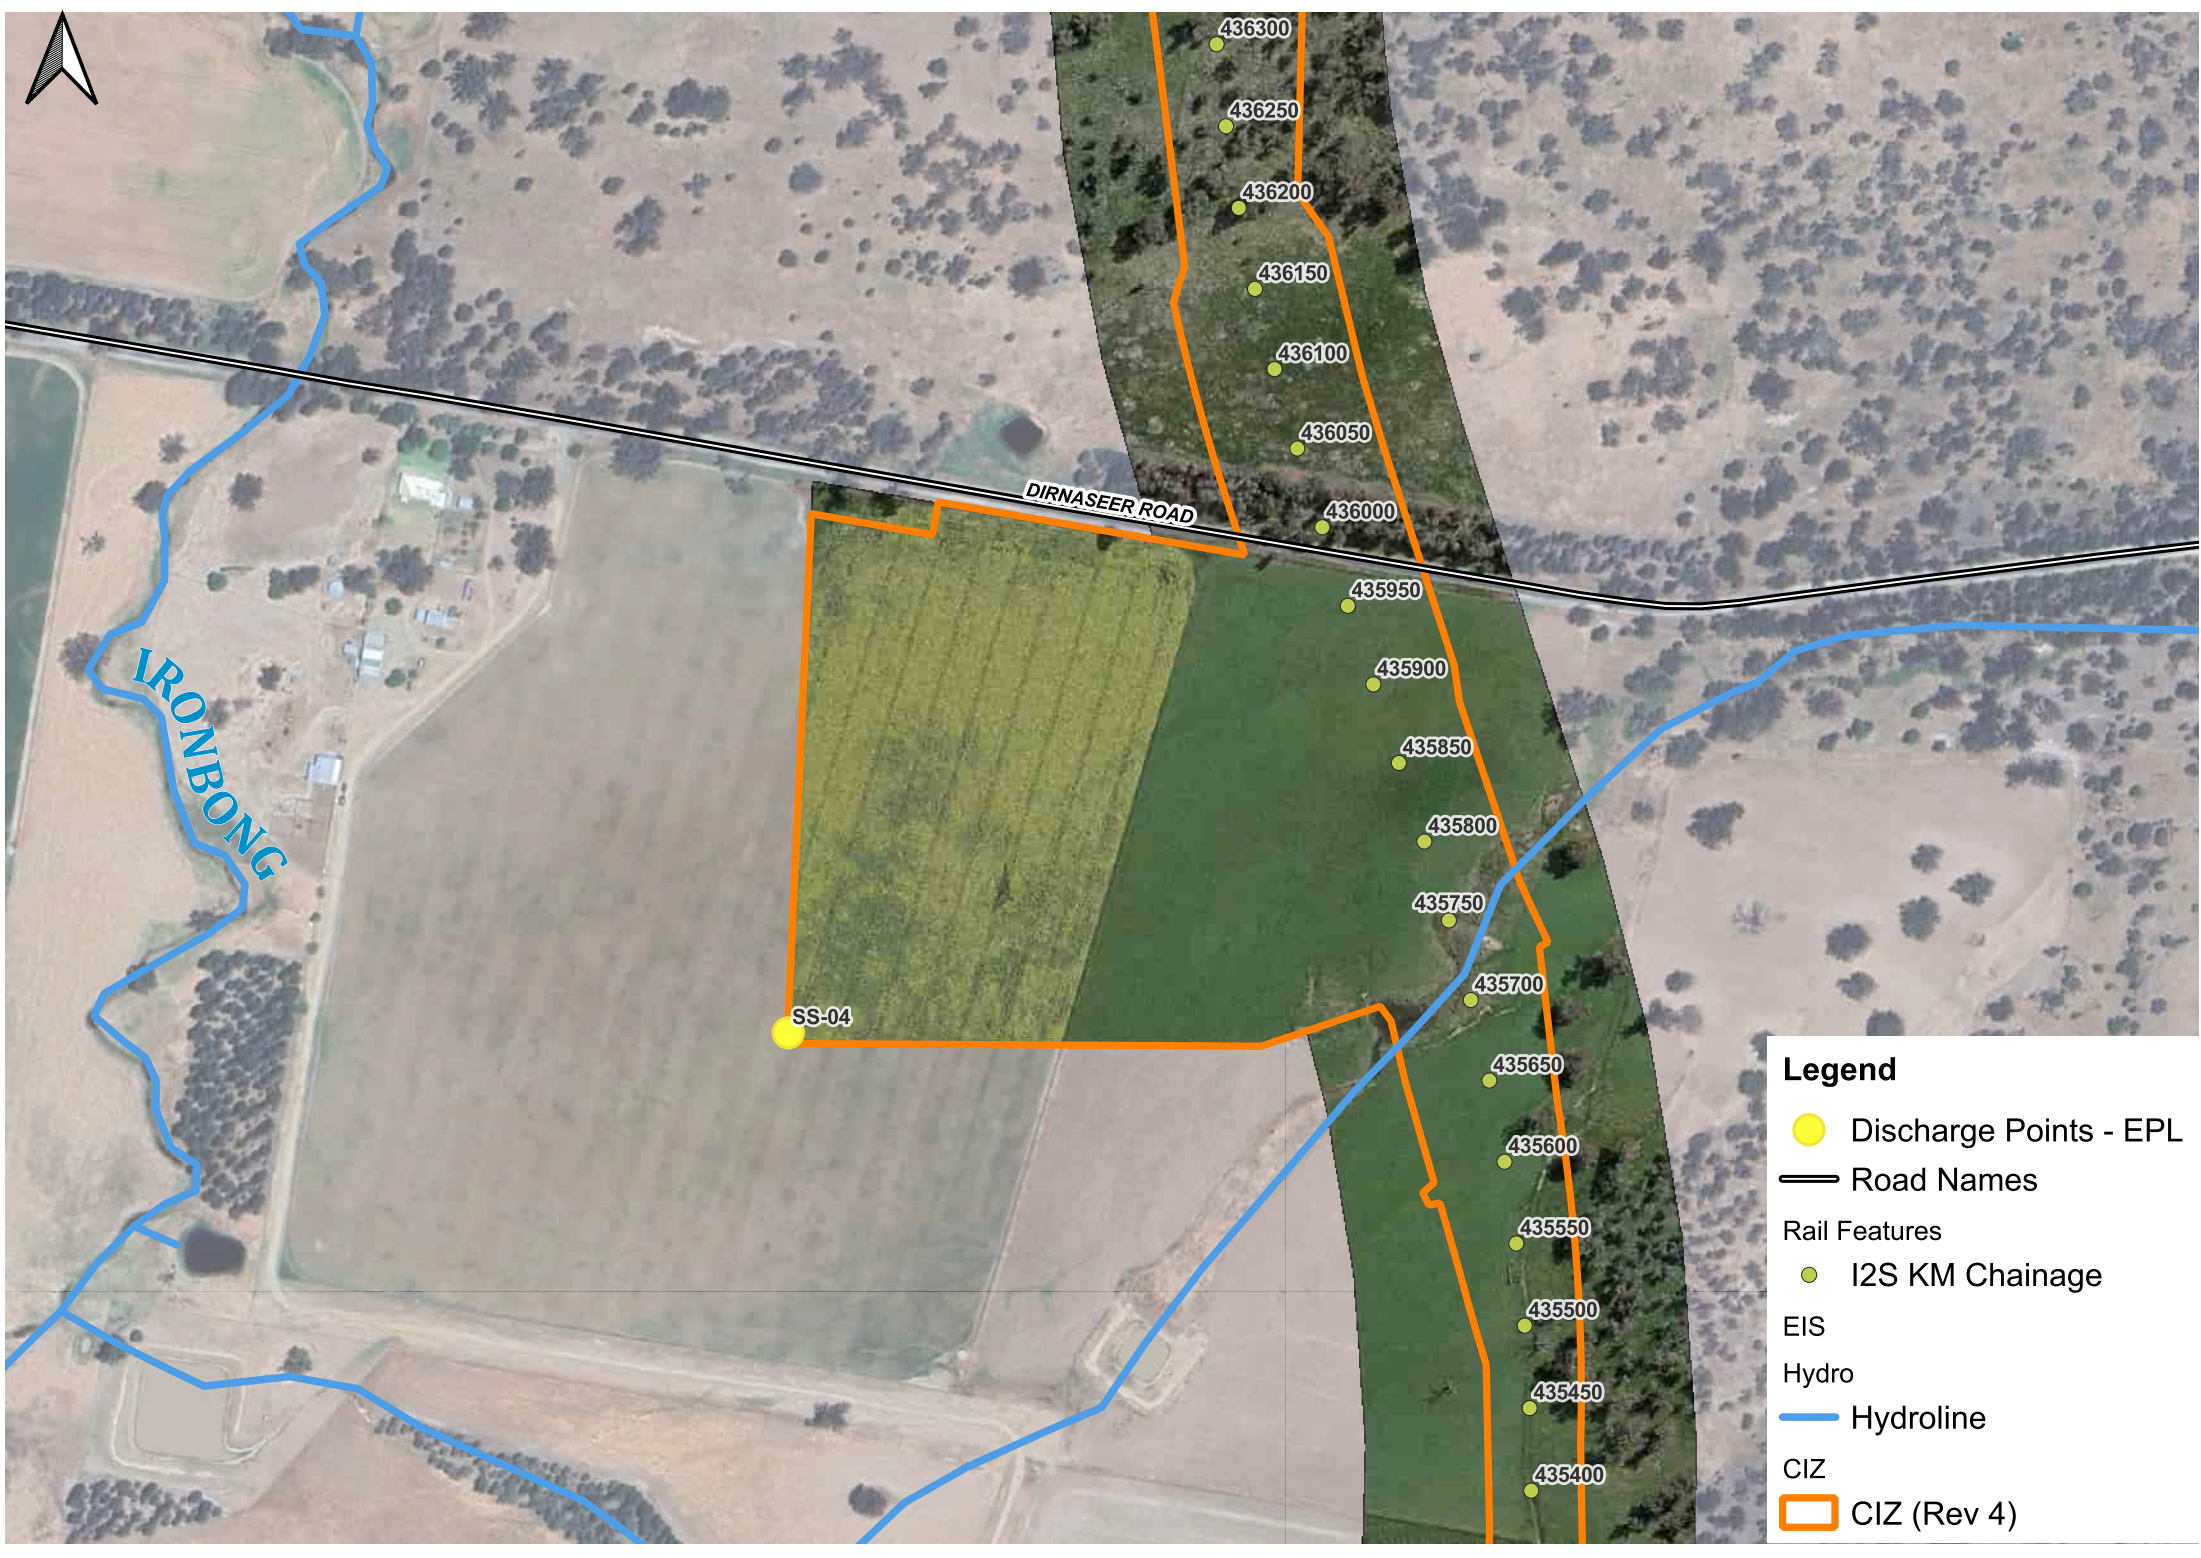

IRONBONG


DIRNASEER ROAD

SS-04

436300  
436250  
436200  
436150  
436100  
436050  
436000  
435950  
435900  
435850  
435800  
435750  
435700  
435650  
435600  
435550  
435500  
435450  
435400

**Legend**

- Discharge Points - EPL
- Road Names
- Rail Features
  - I2S KM Chainage
- EIS
- Hydro
- Hydroline
- CIZ
- CIZ (Rev 4)

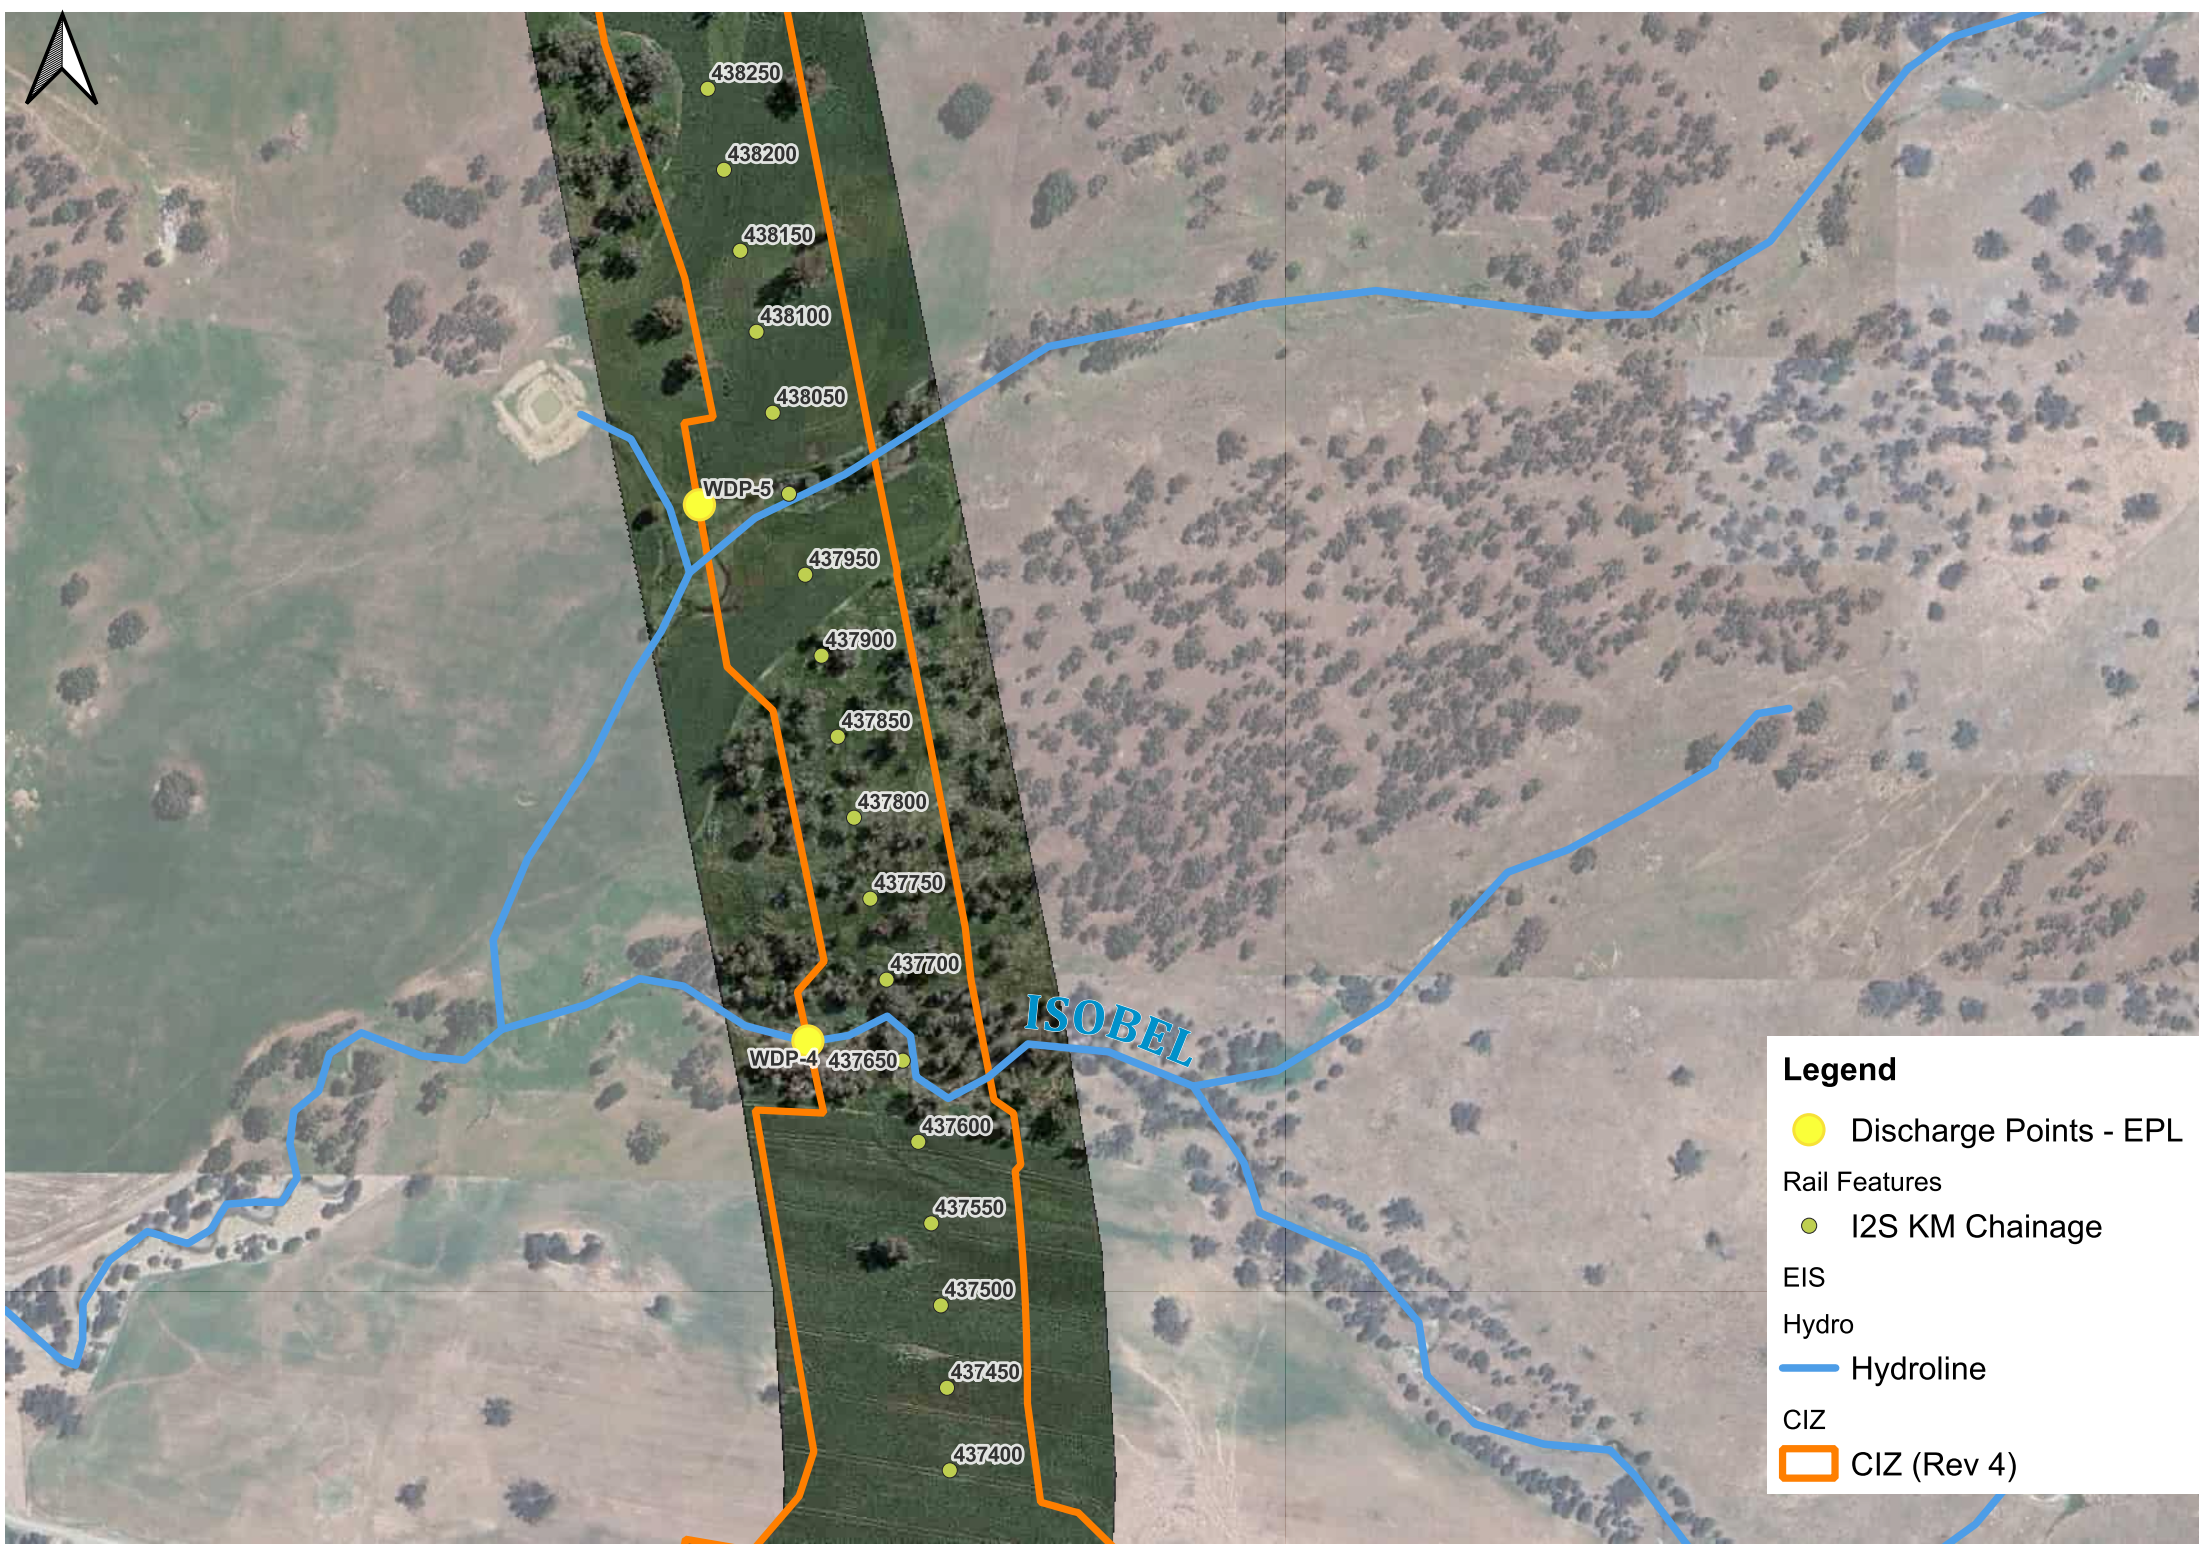

**Legend**

-  Discharge Points - EPL
- Rail Features
  -  I2S KM Chainage
- EIS
  - Hydro
    -  Hydroline
  - CIZ
    -  CIZ (Rev 4)

IRONBONG

SS-05

SS-08

440950  
440900  
440850  
440800  
440750  
440700  
440650  
440600  
440550  
440500  
440450  
440400  
440350  
440300  
440250  
440200  
440150  
440100  
440050

### Legend

● Discharge Points - EPL

Rail Features

● I2S KM Chainage

EIS

Hydro

— Hydroline

CIZ

□ CIZ (Rev 4)



**Legend**

-  Discharge Points - EPL
-  Road Names
- Rail Features
  -  I2S KM Chainage
- EIS
- Hydro
  -  Hydroline
- CIZ
  -  CIZ (Rev 4)



**Legend**

Discharge Points - EPL

Rail Features

I2S KM Chainage

EIS

Hydro

Hydroline

CIZ

CIZ (Rev 4)



DUDAUMAN

WDP-7

**Legend**

- Discharge Points - EPL
- Rail Features
- I2S KM Chainage
- EIS
- Hydro
- Hydroline
- CIZ
- CIZ (Rev 4)



### Legend

● Discharge Points - EPL

== Road Names

Rail Features

● I2S KM Chainage

CIZ

▭ CIZ (Rev 4)
