

M7- M12 Integration Project Environment Protection Licence – Environmental Monitoring Data Report

May 2026



Document Control

Date	04 June 2026
Document No.	M7M12UDC-JHGRP-M7A-EN-RPT-000053
Title	Environment Protection Licence – Environmental Monitoring Data Report May 2026

Document History and Status

Rev	Rev Date	Description	Author	Checked	Reviewed	Approved
01	04/06/2026	For publication	K. Hernandez	D. Windnagel	A. Major	For publication

Contents

1	Project summary	2
2	Environmental Protection Licence and Reporting Requirements	4
3	Noise and vibration monitoring	5
3.1	Noise monitoring	5
3.2	Vibration monitoring	7
4	Discharge Water Quality Monitoring	8

Figures

Figure 1-1	M7-M12 Integration Project.....	3
------------	---------------------------------	---

Tables

Table 3-1	Noise monitoring data	6
-----------	-----------------------------	---


1 Project summary

The M7 Motorway (Modification 6 Widening; SSI-663-Mod-6) (M7 Widening) and the M12 East package of the M12 Motorway project (SSI 9364) will be delivered together under what is referred to as the M7-M12 Integration project (the Project) (refer to Figure 1-1) by John Holland.

The M12 Motorway extends between the M7 Motorway at Cecil Hills and The Northern Road at Luddenham, over a distance of about 16 km. It will be delivered in multiple packages including the M12 West package, M12 Central package and M12 East package (this package is part of the M7-M12 Integration project). The M12 East package involves two components of work:

- Connecting Elizabeth Drive to the M12 Motorway and the upgrade of approximately two kilometres of Elizabeth Drive from east of Duff Road to 300 metres east of the M7 Motorway
- Providing a grade separated motorway to motorway connection between the M7 Motorway and M12 Motorway.

The M7 Widening project will enable the construction and operation of an additional lane in both directions within the existing median of the Westlink M7 for approximately 26 kilometres (km). Works will occur from about 140 metres (m) south of the Kurrajong Road overhead bridge at Prestons (southern end) to the Richmond Road interchange at Oakhurst/Glendenning (northern end), excluding widening through the Westlink M7/M4 Motorway (Light Horse) Interchange.

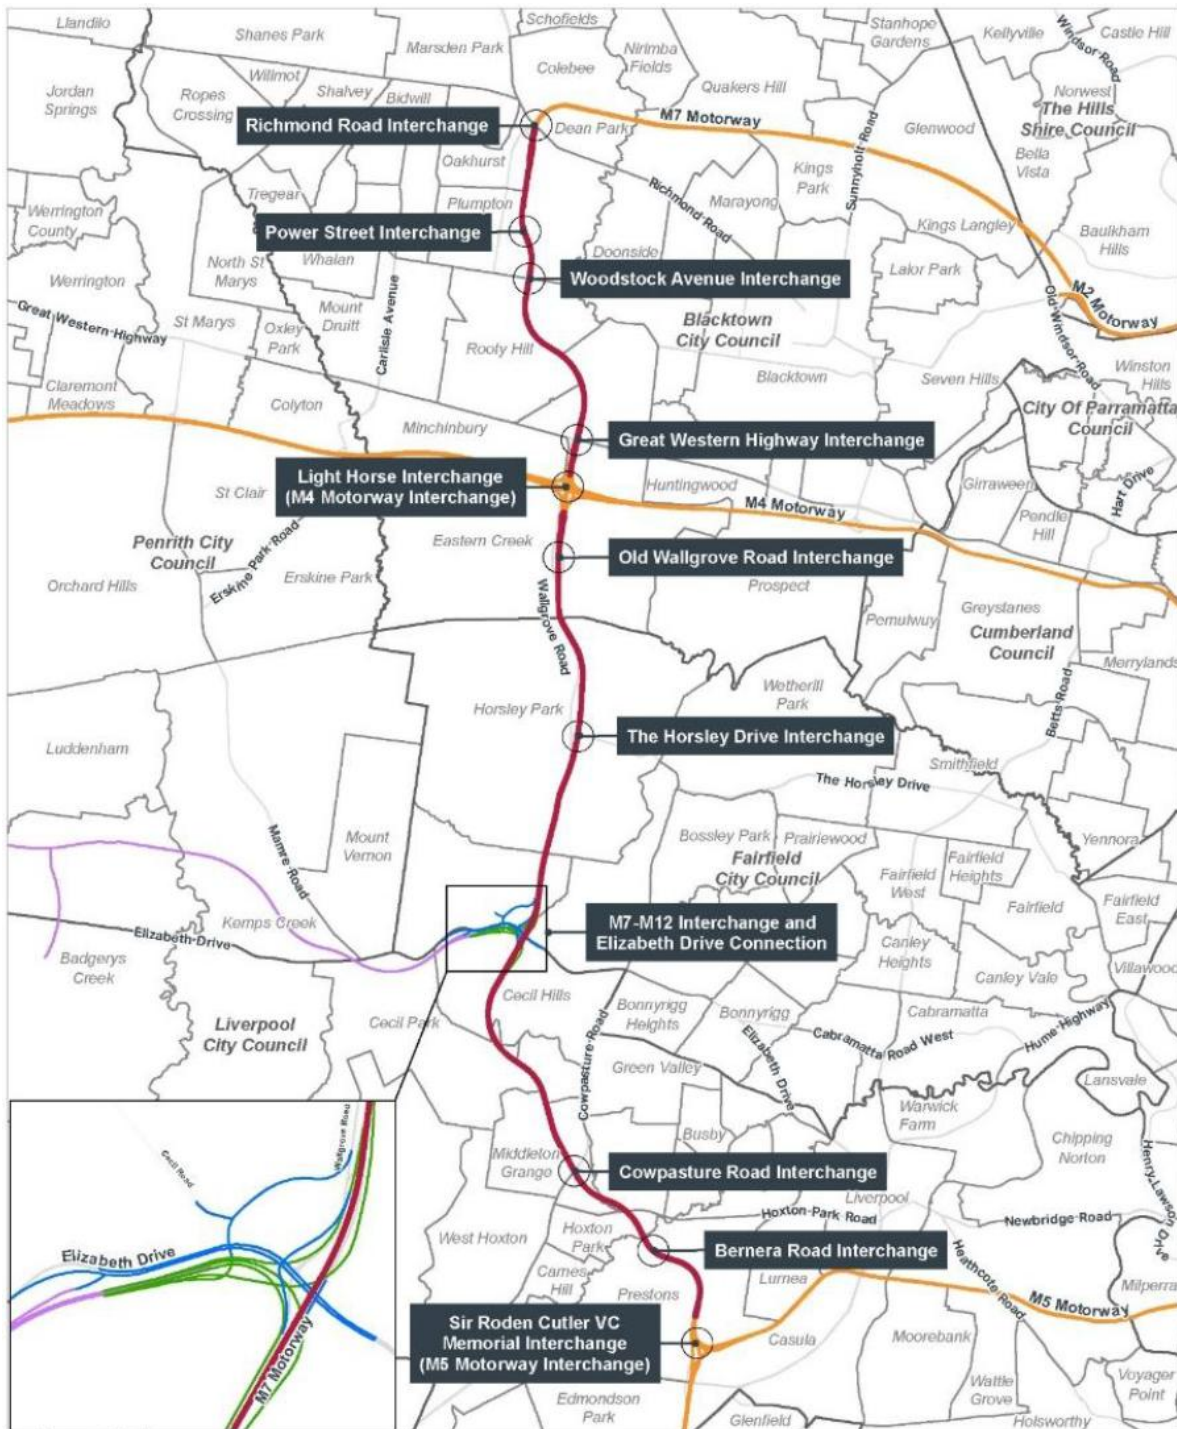

M7-M12 INTEGRATION PROJECT
LOCATION OVERVIEW



Legend

- M7 Widening
- M7-M12 Interchange
- Elizabeth Drive Connection
- M12 Motorway
- Existing motorway
- Interchange
- LGA boundary
- Suburb boundary

Copyright © 2023 AECOM. All rights reserved. This document is the property of AECOM and is intended for the use of the client only. It is not to be distributed, copied, or reproduced in any form without the prior written consent of AECOM. AECOM and its employees, agents, and consultants shall not be held liable for any errors or omissions in this document. The information contained herein is for informational purposes only and does not constitute an offer of any financial product or service. For more information, please contact your AECOM account manager.

The terms of Councils' Conditions of Sale apply to this project. For more information, please refer to the Council's Conditions of Sale.

Neither AECOM Australia Pty Ltd nor AECOM Australia Pty Ltd's employees, agents, or consultants make any representation or warranty of any kind about the accuracy, reliability, completeness, or suitability of this information for the purposes intended, or for any other purpose, without the prior written consent of AECOM Australia Pty Ltd. AECOM Australia Pty Ltd and its employees, agents, and consultants shall not be held liable for any errors or omissions in this document. The information contained herein is for informational purposes only and does not constitute an offer of any financial product or service. For more information, please contact your AECOM account manager.

Source: Transport NSW, 2023

Figure 1-1 M7-M12 Integration Project

2 Environmental Protection Licence and Reporting Requirements

John Holland Pty Ltd obtained the Environment Protection Licence (EPL No. 21829) from the NSW Environment Protection Authority for the project. The licence is for road construction as defined under Schedule 1 of the *Protection of the Environment Operations Act 1997* (POEO Act).

The licence describes monitoring and reporting requirements for the Works. The following report details environmental monitoring undertaken during the May 2026 monitoring period conducted in accordance with the EPL.

The EPL can be found by following the link below to the EPA's website: epa.nsw.gov.au.

3 Noise and vibration monitoring

3.1 Noise monitoring

Noise monitoring was undertaken during the reporting period in accordance with the requirements of the M7M12 Construction Noise and Vibration Monitoring Program (M712UDC-JHGRP-M7A-EN-PLN-000074).

All works were deemed compliant as they complied with applicable criteria, monitoring was predominantly dominated by project works and background noise sources such as local traffic and are detailed in Table 3-1.

Table 3-1 Noise monitoring data

Location Description	Monitoring date	Monitoring period	NCA	Attended or Continuous	Parameter	Measured value dB(A)	Goals and targets dB(A)	Project OOHW Compliance	Comments/Field Observations
30 Bangalow Place, Hoxton Park	20/05/2026	Night	NCA_08	Attended	LAeq (15 min)	58.3	55	JH Works Compliant	Dominant noise source was traffic from local roads. Works were inaudible during monitoring period. JHG works compliant.
33 Isabel Street, Cecil Hills	24/05/2026	Night	NCA_16b	Attended	LAeq (15 min)	49.5	42	JH Works Compliant	Dominant noise source was traffic from local roads. Works were inaudible during monitoring period. JHG works compliant.

Note:

1. LAeq (15min) - The A-weighted equivalent continuous (energy average) A-weighted sound pressure level over a 15-minute period.
2. dBA - Decibels using the A-weighted scale measured according to the frequency of the human ear.
3. PNL: Predicted Noise Level as determined within the relevant CNVIS.

3.2 Vibration monitoring

No vibration monitoring was undertaken during the reporting period as no new vibration intensive works were undertaken within the zone of influence to any sensitive receivers, or the activities had been monitored previously and confirmed to be compliant with the M7M12 Construction Noise and Vibration Monitoring Program.

4 Discharge Water Quality Monitoring

No offsite discharge occurred during May 2026 from sediment basins across the Project.

Majority of basins have been decommissioned and drainage infrastructure completed across the Project.
